



**SAFE CLEAN
WATER PROGRAM**

Regional Program FY24-25 Annual Report Summary

SAFE CLEAN WATER PROGRAM

February 18, 2026

SOUTH SANTA MONICA BAY (SSMB)



Reporting Requirements

Infrastructure Project Developers and Scientific Study Developers are required to prepare Mid-Year (previously Quarterly) and Annual Progress/Expenditure Reports.

Reports are submitted to their respective Watershed Area Steering Committee to be evaluated on **whether the schedules, budget, scopes, and expected benefits have significantly changed or remain consistent** with the Safe, Clean Water Program goals.


Safe Clean Water Reporting Module



[Click Here! ↑](#)

The Reporting Repository houses:

- Regional Program Infrastructure Project/Scientific Studies Applications and completed Reports
- Completed Municipal Program Annual Plans and Reports
- SCW Program Reports

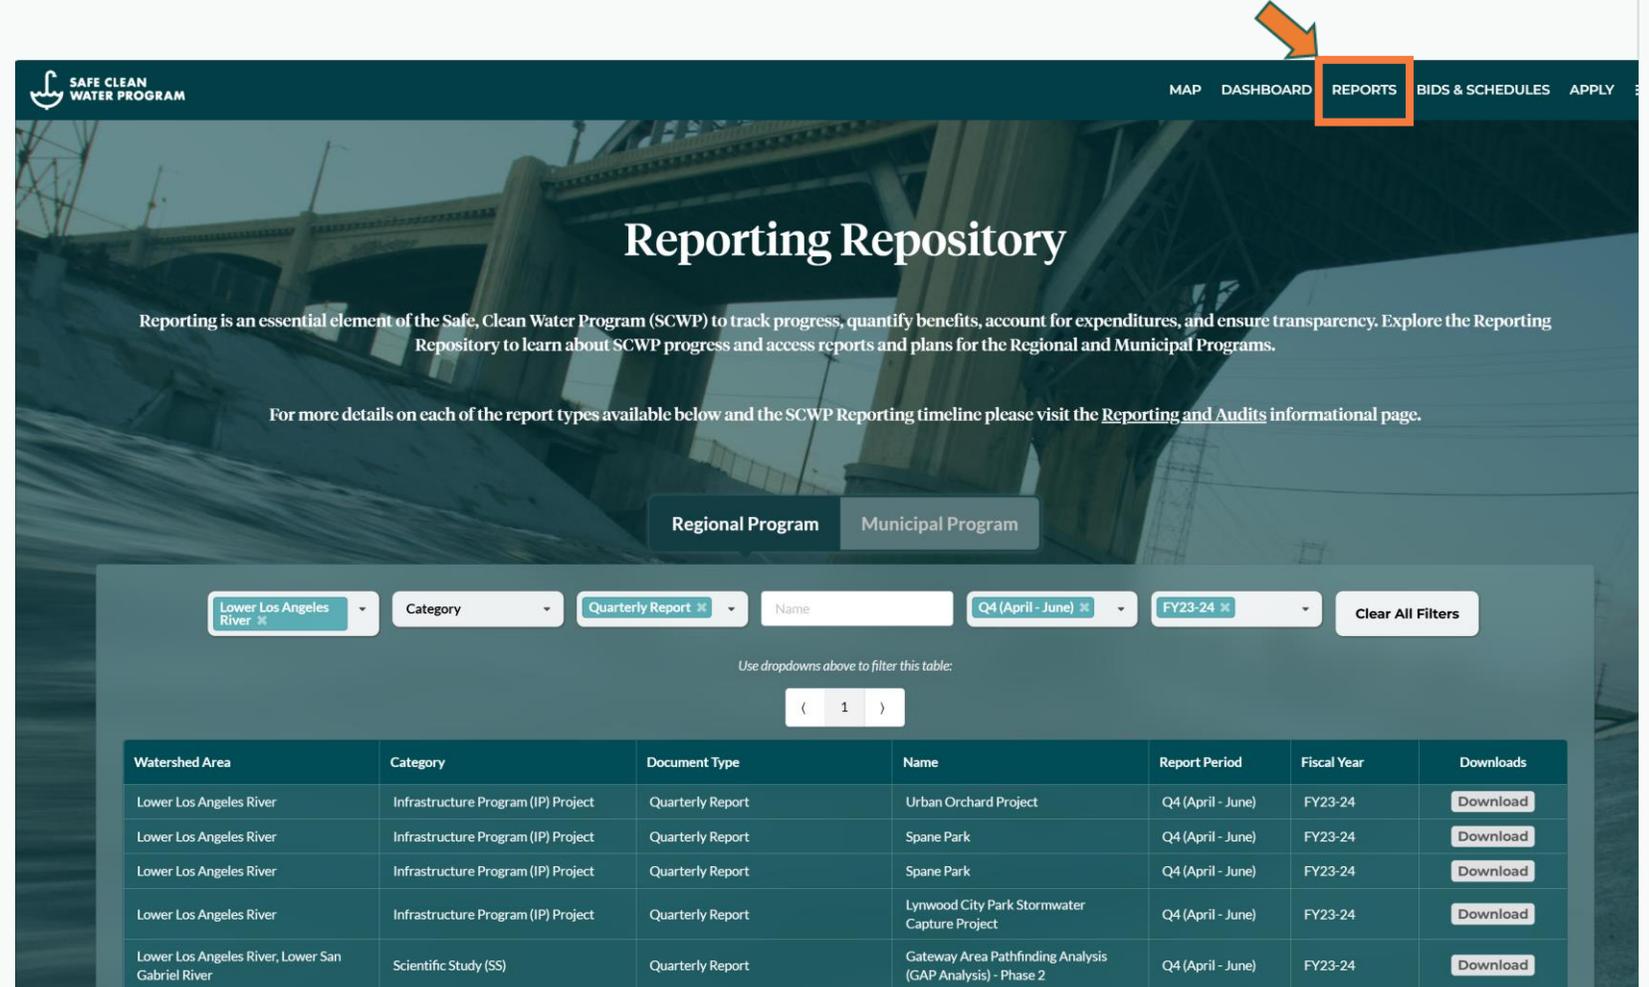

Reporting Repository

Reporting is an essential element of the Safe, Clean Water Program (SCWP) to track progress, quantify benefits, account for expenditures, and ensure transparency. Explore the Reporting Repository to learn about SCWP progress and access reports and plans for the Regional and Municipal Programs.

For more details on each of the report types available below and the SCWP Reporting timeline please visit the [Reporting and Audits](#) informational page.

Regional Program | Municipal Program

Lower Los Angeles River | Category | Quarterly Report | Name | Q4 (April - June) | FY23-24 | Clear All Filters

Use dropdowns above to filter this table:

Watershed Area	Category	Document Type	Name	Report Period	Fiscal Year	Downloads
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Urban Orchard Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Lynwood City Park Stormwater Capture Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River, Lower San Gabriel River	Scientific Study (SS)	Quarterly Report	Gateway Area Pathfinding Analysis (GAP Analysis) - Phase 2	Q4 (April - June)	FY23-24	Download

Recent and Upcoming Project Developer Deadlines

PROJECT DEVELOPER REPORT	REPORTING PERIOD	DUE DATE	WASC REVIEW
FY24-25 Annual Report	July 2024 – June 2025	Aug 15, 2025	Winter 2025/2026
FY25-26 Mid-Year	July 2025 – December 2025	Feb 15, 2026	Spring/Summer 2026
FY25-26 Annual Report	July 2025 – June 2026	Aug 15, 2026	Winter 2026/2027
FY26-27 Mid-Year	July 2026 – December 2026	Feb 15, 2027	Spring/Summer 2027

WASC Role in reviewing Progress/Expenditure Reports

Progress/Expenditure Reports

- WASCs are responsible for reviewing progress/expenditure reports submitted by Developers for funded Projects/ Studies to evaluate:
 - Changes in schedules, scopes, expected benefits
 - If efforts remain consistent with SCW Program Goals
- Developers are requested to attend WASC meetings to describe the current project status and respond to questions about reported activities

This reporting period summary covers **July 1, 2024 to June 30, 2025** for Projects and Studies approved in FY20-21 through FY24-25 Stormwater Investment Plans

WASC Funding Overview as of 6/30/2025

Reporting Period FY24-25:

Regional reports due 45 days after end of reporting period. 

- **Annual Reporting Period**
July 1, 2024 – June 30, 2025

Total Anticipated SCW Funding

\$122,391,016

Total Funds Awarded to Date

\$81,663,298

Total Funds Received to Date

\$64,863,042

Total Reported Expenditures To Date

\$29,492,343

WASC Funding Overview as of 6/30/2025

WASC Funding Definitions:

- **Total Anticipated SCW Funding:** Total SCW Funding Budgeted and Projected in FY20-21 through FY24-25 Stormwater Investment Plans (SIPs).
- **Total Funds Awarded to Date:** Total budgeted in FY20-21 through FY24-25 SIPs. This is the maximum amount that a Project Developer may have received at the time of submitting FY24-25 Annual Reports.
- **Total Funds Received to Date:** Total budgeted funds that the Project or Study has received through the execution of the Funds Transfer Agreement(s).
- **Total Reported Expenditures:** The total amount of expenditures reported by the Project/Study Developer as of 6/30/2025.

WASC Funding Overview as of 6/30/2025 (Slide 1 of 3)

PROJECT OR STUDY NAME	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Alondra Park Multi Benefit Stormwater Capture Project	\$30,000,000	\$30,000,000	\$30,000,000	\$20,589,332
Beach Cities Green Streets Project	\$5,366,953	\$5,366,953	\$5,366,953	\$0
Carson Stormwater and Runoff Capture Project at Carriage Crest Park	\$1,037,500	\$830,000	\$622,500	\$0
Downtown Lomita Multi-Benefit Stormwater Project	\$449,300	\$449,300	\$449,300	\$402,725
Fulton Playfield Multi-Benefit Infiltration Project	\$4,292,138	\$3,849,000	\$2,166,000	\$361,030
Glen Anderson Park Regional Stormwater Capture Green Streets	\$782,000	\$782,000	\$391,000	\$217,717
Hermosa Beach Multi-Benefit Parking Lot Greening Project (Lot D) ¹	\$423,950	\$423,950	\$423,950	\$0
Identifying Best Practices for Maintaining Stormwater Drywell Capacity (SSMB)	\$408,871	\$79,989	\$0	\$0

¹ This project has been withdrawn by the Developer in FY24-25 and no report is needed for future reporting periods.

WASC Funding Overview as of 6/30/2025 (Slide 2 of 3)

PROJECT OR STUDY NAME	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Machado Lake Ecosystem Rehabilitation (MLER) Operations and Maintenance	\$3,199,371	\$1,077,586	\$1,077,586	\$0
Microplastics in LA County Stormwater (SSMB)	\$247,752	\$247,752	\$171,602	\$130,447
Recalculation of Wet Weather Zinc Criterion (SSMB)	\$57,886	\$57,886	\$57,886	\$52,713
Regional Pathogen Reduction Study (SSMB)	\$1,109,563	\$1,054,085	\$0	\$0
South Santa Monica Bay Water Quality Enhancement: 28th Street Storm Drain Infiltration Project	\$17,620,030	\$13,564,298	\$9,508,565	\$1,226,031
Stormwater Basin Expansion Project	\$4,505,000	\$4,505,000	\$4,505,000	\$4,175,689
Street Sweeping Study (SSMB)	\$113,100	\$46,400	\$0	\$0
Torrance Airport Storm Water Basin Project	\$19,190,402	\$450,000	\$450,000	\$0

WASC Funding Overview as of 6/30/2025 (Slide 3 of 3)

PROJECT OR STUDY NAME	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Torrance Airport Storm Water Basin Project, Phase 2	\$906,000	\$906,000	\$906,000	\$635,772
West Rancho Dominguez - San Pedro Street Green Improvement	\$800,000	\$800,000	\$800,000	\$0
Wilmington Neighborhood Greening Project	\$16,683,000	\$10,373,800	\$1,167,400	\$1,113,788
Wilmington Q Street Local Urban Area Flow Management Project	\$4,923,700	\$4,923,700	\$4,923,700	\$587,099
Wilmington-Anaheim Green Infrastructure Corridor Project	\$10,274,500	\$1,875,600	\$1,875,600	\$0

FY24-25 – Annual Report Status

Number of Infrastructure Projects (IP)

INFRASTRUCTURE PROJECT REPORT STATUS	NUMBER OF PROJECTS
Concluded Project	0
Completed	16
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
TOTAL	16

Number of Scientific Studies (SS)

SCIENTIFIC STUDIES REPORT STATUS	NUMBER OF STUDIES
Concluded Study	0
Completed	5
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
TOTAL	5

List of Infrastructure Program Projects by Phase as of 6/30/2025 (Slide 1 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Alondra Park Multi Benefit Stormwater Capture Project			X		
Beach Cities Green Streets Project		X			
Carson Stormwater and Runoff Capture Project at Carriage Crest Park				X	
Downtown Lomita Multi-Benefit Stormwater Project	X				
Fulton Playfield Multi-Benefit Infiltration Project	X				
Glen Anderson Park Regional Stormwater Capture Green Streets	X				

List of Infrastructure Program Projects by Phase as of 6/30/2025 (Slide 2 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Hermosa Beach Multi-Benefit Parking Lot Greening Project (Lot D)		X			
Machado Lake Ecosystem Rehabilitation (MLER) Operations and Maintenance				X	
South Santa Monica Bay Water Quality Enhancement: 28th Street Storm Drain Infiltration Project	X				
Stormwater Basin Expansion Project					X
Torrance Airport Storm Water Basin Project	X				

List of Infrastructure Program Projects by Phase as of 6/30/2025

(Slide 3 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Torrance Airport Storm Water Basin Project, Phase 2	X				
West Rancho Dominguez - San Pedro Street Green Improvement	X				
Wilmington Neighborhood Greening Project	X				
Wilmington Q Street Local Urban Area Flow Management Project	X				
Wilmington-Anaheim Green Infrastructure Corridor Project	X				

List of Infrastructure Program Projects and Scientific Studies Completed as of 6/30/2025

PROJECT OR STUDY NAME	PROJECT TYPE
Recalculation of Wet Weather Zinc Criterion	Scientific Study

Accomplishments

Beach Cities Green Streets Project



Owner: City of Torrance

Construction Start: 7/21/2025

Construction Completion: 2/28/2026

Project Phase: Bid / Award



Project Updates

- February 2025 - Project was advertised for bids.
- May 2025 - Construction contract was awarded.



Project Highlights

- This project was initiated to improve the water quality for the Santa Monica Bay Beaches using permeable pavement and dry wells which will intercept, filter, and infiltrate stormwater.

PUBLIC WORKS AGREEMENT

This PUBLIC WORKS AGREEMENT ("Agreement") is made and entered into as of MAY 6, 2025 (the "Effective Date"), by and between the CITY OF TORRANCE, a municipal corporation ("CITY"), and [REDACTED] a California Corporation ("CONTRACTOR").

RECITALS:

- A. The CITY wishes to retain the services of an experienced and qualified CONTRACTOR to construct the **Beach Cities Green Streets Project, S-194 & B2025-04**;
- B. In order to obtain the desired services, The CITY has circulated a Notice Inviting Bids for the construction of the **Beach Cities Green Streets Project, S-194 & B2025-04** (the "NIB"); and
- C. CONTRACTOR has submitted a Bid (the "Bid") in response to the NIB. CONTRACTOR represents that it is qualified to perform those services requested in the Plans and Specifications. Based upon its review of all Bids submitted in response to the NIB, The CITY is willing to award the contract to CONTRACTOR.

AGREEMENT:

1. SERVICES TO BE PERFORMED BY CONTRACTOR

CONTRACTOR will provide the services and install those materials listed in the Plans and Specifications, which are on file in the Public Works Department. The NIB and the Plans and Specifications are made a part of this Agreement. A copy of the Bid is attached as Exhibit A.

2. TERM

Unless earlier terminated in accordance with Paragraph 4 below, this Agreement will continue in full force and effect for two years from the Effective Date.

Accomplishments

Stormwater Basin Expansion Project



Owner: City of Torrance

Construction Start: 9/29/2022

Construction Completion: 11/16/2023

Project Phase: O&M / Post-Construction
Monitoring



Project Updates

- April 2025 – A consultant firm was selected for post-construction monitoring, and a contract was fully executed.
- City completed procurement of backup pumps.



Project Highlights

- This project aims to retain and treat dry-weather stormwater flows and runoff by improving three flood control basins.



City of Torrance, Public Works Department

Request for Quotation – Not an Order

Buyer: Turquoise Benjamin or e-mail to TBenjamin@TorranceCA.Gov

Quotation Due By: Noon, December 4, 2024. Late Quotations Will Not Be Evaluated.

Ref: Stormwater Basin Expansion Project, I-179 Monitoring and Reporting Services

This RFQ is requesting quotes from qualified vendors for **Stormwater Basin Expansion Project, I-179 Monitoring and Reporting Services**. This RFQ is intended to be as descriptive as possible. However, Proposers may not take advantage of omissions or oversights in this document. Proposers must supply products and services that meet or exceed the requirements of this RFQ. In the event of a dispute over installation or performance, the needs of the City of Torrance will govern. Quotations must be submitted on this form filled out completely. Vendors that do not fill out the City RFQ form will not be considered.

The City of Torrance:

The City of Torrance is on the western side of Los Angeles County. It is bordered by the Palos Verdes Peninsula on the south, the City of Gardena on the north, the City of Redondo Beach on the north and west boundaries, the City of Lomita on the east and the Pacific Ocean on the west. The City encompasses an area of approximately 21 square miles, 329 miles of Streets, 1870 intersections, 550 miles of sidewalks, 47,000 Street Trees, 6 Public Libraries, a Municipal Airport, Transit System, 46 Parks & Recreation Amenities, 6 Fire Stations, 1 Police Station and 1 Police Community Center, and has an estimated population of approximately 146,115, which makes Torrance one of the top 10 cities in Los Angeles County in regards to population.

The successful Vendor will be issued a Purchase Order for the services required and will include the terms and conditions attached to this RFQ.

- The State of California Senate Bill 7 (SB7) for prevailing wage applies to construction contracts over \$25,000 and contracts for alteration, demolition, repair and maintenance over \$15,000. There are no exemptions.
- List and describe all applicable fees. Fees not listed below will not be authorized for payment on any invoices throughout the term of the purchase order.
- The vendor must provide certificates of insurance and/or endorsements indicating appropriate coverage to the City of Torrance Public Works Department before a Purchase Order will be awarded as per this Request for Quotation. The CITY, the City Council and each member thereof, members of boards and commissions, every officer, agent, official, employee and volunteer must be named as additional insured under the automobile and general liability policies.
- Prior to the issuance of a purchase order, the vendor must submit to the City of Torrance Public Works Department proof of a City of Torrance Business License if your company is located in the City of Torrance; will physically be working in the City of Torrance; or will be using your own vehicles to deliver to the City of Torrance. For additional information and licensing requirements, please contact the City of

Critical Issues

(Slide 1 of 1)

PROJECT NAME	ACTIVITY DELAYS / CONCERNS
Carson Stormwater and Runoff Capture Project at Carriage Crest Park	Schedule Delay
Fulton Playfield Multi-Benefit Infiltration Project	Schedule Delay
Glen Anderson Park Regional Stormwater Capture Green Streets	Schedule Delay
Hermosa Beach Multi-Benefit Parking Lot Greening Project (Lot D)	Project Withdrawal
South Santa Monica Bay Water Quality Enhancement: 28 th Street Storm Drain Infiltration Project	Schedule Delay, CEQA In Progress
Wilmington Neighborhood Greening Project	CEQA In Progress
Wilmington Q Street Local Urban Area Flow Management Project	Schedule Delay
Wilmington-Anaheim Green Infrastructure Corridor Project	Schedule Delay

Questions?





Thank you

QUESTIONS?

Contact:

Eric Bonilla, PE (SafeCleanWaterLA@pw.lacounty.gov & ebonilla@dpw.lacounty.gov)

For inquiries related to reporting, SCWPReporting@hdrinc.com

For other inquires, SafeCleanWaterLA@pw.lacounty.gov
