



**SAFE CLEAN  
WATER PROGRAM**

# Regional Program FY24-25 Annual Report Summary

**SAFE CLEAN WATER PROGRAM**

**March 26, 2026**

**UPPER SAN GABRIEL RIVER (USGR)**



# Reporting Requirements

Infrastructure Project Developers and Scientific Study Developers are required to prepare Mid-Year (previously Quarterly) and Annual Progress/Expenditure Reports.

Reports are submitted to their respective Watershed Area Steering Committee to be evaluated on **whether the schedules, budget, scopes, and expected benefits have significantly changed or remain consistent** with the Safe, Clean Water Program goals.


## Safe Clean Water Reporting Module



[Click Here! ↑](#)

# The Reporting Repository houses:

- Regional Program Infrastructure Project/Scientific Studies Applications and completed Reports
- Completed Municipal Program Annual Plans and Reports
- SCW Program Reports



Reporting is an essential element of the Safe, Clean Water Program (SCWP) to track progress, quantify benefits, account for expenditures, and ensure transparency. Explore the Reporting Repository to learn about SCWP progress and access reports and plans for the Regional and Municipal Programs.

For more details on each of the report types available below and the SCWP Reporting timeline please visit the [Reporting and Audits](#) informational page.

Regional Program    Municipal Program

Lower Los Angeles River    Category    Quarterly Report    Name    Q4 (April - June)    FY23-24    Clear All Filters

Use dropdowns above to filter this table:

( 1 )

Watershed Area	Category	Document Type	Name	Report Period	Fiscal Year	Downloads
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Urban Orchard Project	Q4 (April - June)	FY23-24	<a href="#">Download</a>
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	<a href="#">Download</a>
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	<a href="#">Download</a>
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Lynwood City Park Stormwater Capture Project	Q4 (April - June)	FY23-24	<a href="#">Download</a>
Lower Los Angeles River, Lower San Gabriel River	Scientific Study (SS)	Quarterly Report	Gateway Area Pathfinding Analysis (GAP Analysis) - Phase 2	Q4 (April - June)	FY23-24	<a href="#">Download</a>

## Recent and Upcoming Project Developer Deadlines

PROJECT DEVELOPER REPORT	REPORTING PERIOD	DUE DATE	WASC REVIEW
FY24-25 Annual Report	July 2024 – June 2025	Aug 15, 2025	Winter 2025/2026
FY25-26 Mid-Year	July 2025 – December 2025	Feb 15, 2026	Spring/Summer 2026
FY25-26 Annual Report	July 2025 – June 2026	Aug 15, 2026	Winter 2026/2027
FY26-27 Mid-Year	July 2026 – December 2026	Feb 15, 2027	Spring/Summer 2027

## WASC Role in reviewing Progress/Expenditure Reports

### **Progress/Expenditure Reports**

- WASCs are responsible for reviewing progress/expenditure reports submitted by Developers for funded Projects/ Studies to evaluate:
  - Changes in schedules, scopes, expected benefits
  - If efforts remain consistent with SCW Program Goals
- Developers are requested to attend WASC meetings to describe the current project status and respond to questions about reported activities

This reporting period summary covers **July 1, 2024 to June 30, 2025** for Projects and Studies approved in FY20-21 through FY24-25 Stormwater Investment Plans

## WASC Funding Overview as of 6/30/2025

### Reporting Period FY24-25:

Regional reports due 45 days  
after end of reporting period. 

- **Annual Reporting Period**  
July 1, 2024 - June 30, 2025

Total Anticipated SCW Funding

**\$111,812,260**

Total Funds Awarded to Date

**\$88,246,068**

Total Funds Received to Date

**\$67,140,956**

Total Reported Expenditures To Date

**\$25,407,945**

## WASC Funding Overview as of 6/30/2025

### WASC Funding Definitions:

- **Total Anticipated SCW Funding:** Total SCW Funding Budgeted and Projected in FY20-21 through FY24-25 Stormwater Investment Plans (SIPs).
- **Total Funds Awarded to Date:** Total budgeted in FY20-21 through FY24-25 SIPs. This is the maximum amount that a Project Developer may have received at the time of submitting FY24-25 Annual Reports.
- **Total Funds Received to Date:** Total budgeted funds that the Project or Study has received through the execution of the Funds Transfer Agreement(s).
- **Total Reported Expenditures:** The total amount of expenditures reported by the Project/Study Developer as of 6/30/2025.

## WASC Funding Overview as of 6/30/2025 (Slide 1 of 3)

PROJECT OR STUDY NAME	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Barnes Park	\$14,735,690	\$14,735,690	\$14,735,690	\$11,557,083
Bassett High School Stormwater Capture Multi-Benefit Project	\$31,200,000	\$21,200,000	\$10,200,000	\$4,365,284
Community Garden Stormwater Capture Investigation (USGR) <sup>1</sup>	\$378,284	\$378,284	\$378,284	\$119,554
Encanto Park Stormwater Capture Project	\$2,482,248	\$2,482,248	\$702,860	\$451,925
Fairplex	\$2,900,000	\$2,900,000	\$2,900,000	\$945,639
Finkbiner Park Stormwater Capture Project	\$2,581,286	\$2,581,286	\$2,581,286	\$1,021,232
Finkbiner Park Stormwater Capture Project, Construction Phase	\$18,376,246	\$6,152,082	\$0	\$0
Garvey Avenue Grade Separation Drainage Improvement Project	\$4,000,000	\$4,000,000	\$4,000,000	\$4,147,629 <sup>2</sup>

<sup>1</sup> This project has been completed and does not require submission of a progress report for this period.

<sup>2</sup> Pending update confirming why the reported expenditures is larger than the funds received.

# WASC Funding Overview as of 6/30/2025

*(Slide 2 of 3)*

PROJECT OR STUDY NAME	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Glendora Avenue Green Streets	\$315,000	\$315,000	\$0	\$0
Identifying Best Practices for Maintaining Stormwater Drywell Capacity	\$1,022,178	\$199,972	\$199,972	\$151
Lone Hill Park	\$900,000	\$900,000	\$900,000	\$447,204
Marchant Park	\$675,000	\$675,000	\$675,000	\$39,150
Maximizing Impact of Minimum Control Measures (USGR)	\$393,109	\$393,109	\$393,109	\$382,314
Pedley Spreading Grounds	\$2,825,900	\$2,825,900	\$1,587,080	\$620,110
Pelota Park	\$1,325,000	\$1,325,000	\$1,325,000	\$0
Regional Pathogen Reduction Study (USGR)	\$1,139,644	\$619,822	\$0	\$0

## WASC Funding Overview as of 6/30/2025 (Slide 3 of 3)

PROJECT OR STUDY NAME	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
San Gabriel Valley Regional Confirmation of Infiltration Rates <sup>1</sup>	\$385,000	\$385,000	\$385,000	\$366,614
Wingate Park Regional EWMP Project	\$24,177,675	\$24,177,675	\$24,177,675	\$944,056
Zamora Park Renovation	\$2,000,000	\$2,000,000	\$2,000,000	\$0

<sup>1</sup>This project has been completed and does not require submission of a progress report for this period.

## FY24-25 – Annual Report Status

### Number of Infrastructure Projects (IP)

INFRASTRUCTURE PROJECT REPORT STATUS	NUMBER OF PROJECTS
Concluded Project	0
Completed	14
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
<b>TOTAL</b>	<b>14</b>

### Number of Scientific Studies (SS)

SCIENTIFIC STUDIES REPORT STATUS	NUMBER OF STUDIES
Concluded Study	2
Completed	3
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
<b>TOTAL</b>	<b>5</b>

# List of Infrastructure Program Projects by Phase as of 6/30/2025

*(Slide 1 of 2)*

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Barnes Park			X		
Bassett High School Stormwater Capture Multi-Benefit Project	X				
Encanto Park Stormwater Capture Project	X				
Fairplex	X				
Finkbiner Park Stormwater Capture Project	X				
Finkbiner Park Stormwater Capture Project, Construction Phase	X				

## List of Infrastructure Program Projects by Phase as of 6/30/2025 (Slide 2 of 2)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Garvey Avenue Grade Separation Drainage Improvement Project			X		
Glendora Avenue Green Streets	X				
Lone Hill Park	X				
Marchant Park	X				
Pedley Spreading Grounds			X		
Pelota Park	X				
Wingate Park Regional EWMP Project	X				
Zamora Park Renovation Project			X		

## List of Infrastructure Program Projects and Scientific Studies Completed as of 6/30/2025

PROJECT OR STUDY NAME	PROJECT TYPE
Community Garden Stormwater Capture Investigation	Scientific Study
San Gabriel Valley Regional Confirmation of Infiltration Rates	Scientific Study

## Accomplishments Barnes Park



**Owner:** City of Baldwin Park  
**Construction Start:** 9/2023  
**Construction Completion:** 12/2026  
**Project Phase:** Construction



### Project Updates

- Installed electrical, stormwater, irrigation, paving, and park amenity improvements.
- The Caltrans Encroachment/Utility Policy Exception Permit was prepared and submitted.



### Project Highlights

- The project plans to collect, capture, treat, and infiltrate stormwater from a 443-acre drainage area which will reduce flooding and pollutant load for downstream waterbodies.

Basketball Courts



Cistern/Access Vault



Electrical Panel



# Accomplishments

## Encanto Park



**Owner:** City of Baldwin Park  
**Construction Start:** 9/2023  
**Construction Completion:** 12/2026  
**Project Phase:** Construction




### Project Updates

- **June 30, 2025** – MND was completed.
- Design development continued with the 90% design plan set.



### Project Highlights

- The project plans to divert, treat, and infiltrate stormwater and dry-weather flows from existing stormwater infrastructure to improve water supply and water quality for the San Gabriel River.

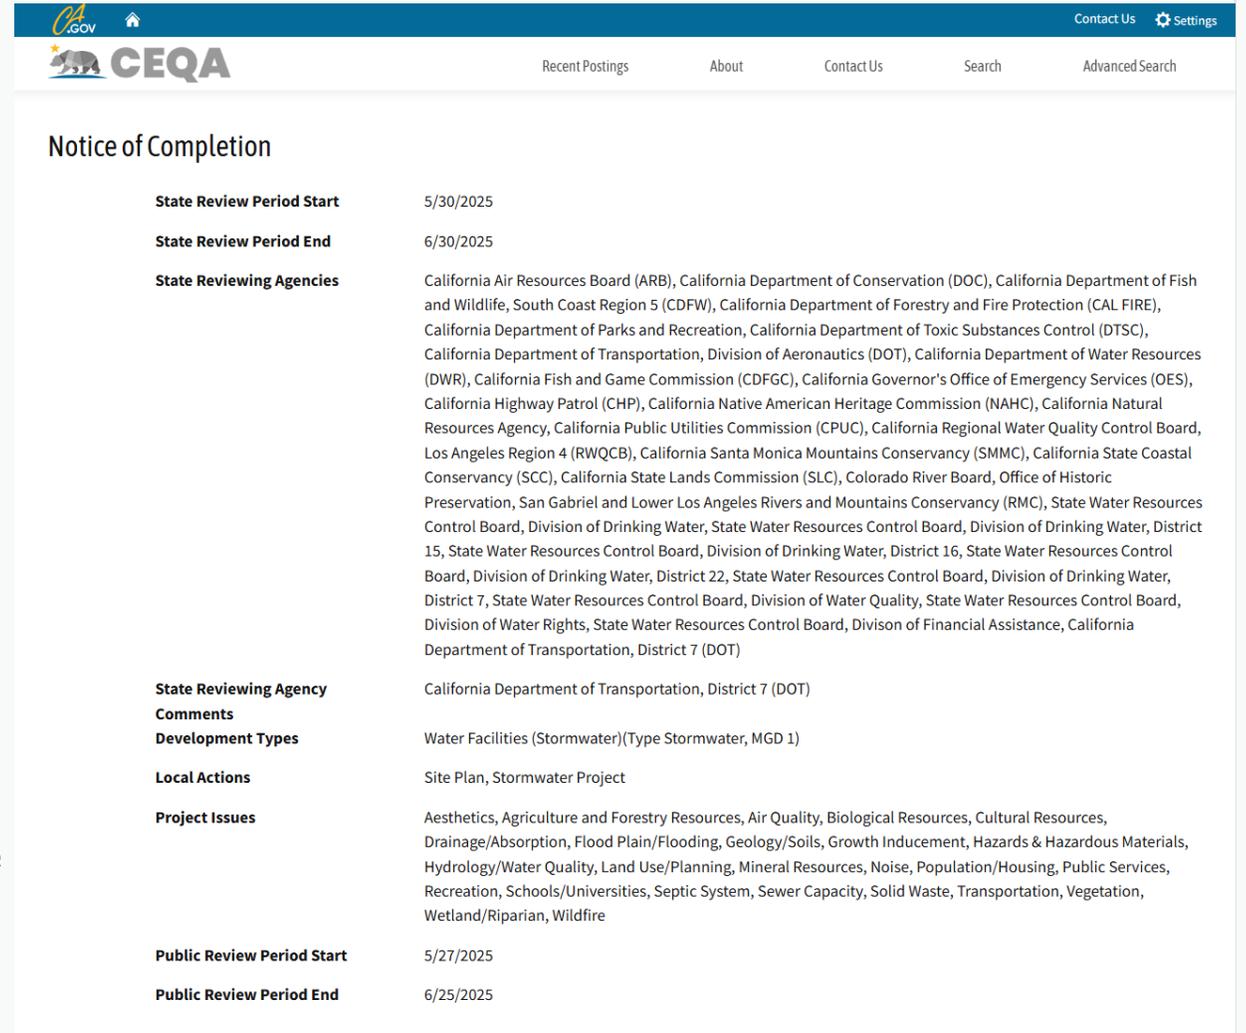

The screenshot shows the CEQA project page for Encanto Park. The header includes the CA.GOV logo, a home icon, and navigation links for Contact Us and Settings. Below the header, there are links for Recent Postings, About, Contact Us, Search, and Advanced Search. The main content area is titled "Notice of Completion" and contains the following information:

<b>State Review Period Start</b>	5/30/2025
<b>State Review Period End</b>	6/30/2025
<b>State Reviewing Agencies</b>	California Air Resources Board (ARB), California Department of Conservation (DOC), California Department of Fish and Wildlife, South Coast Region 5 (CDFW), California Department of Forestry and Fire Protection (CAL FIRE), California Department of Parks and Recreation, California Department of Toxic Substances Control (DTSC), California Department of Transportation, Division of Aeronautics (DOT), California Department of Water Resources (DWR), California Fish and Game Commission (CDFGC), California Governor's Office of Emergency Services (OES), California Highway Patrol (CHP), California Native American Heritage Commission (NAHC), California Natural Resources Agency, California Public Utilities Commission (CPUC), California Regional Water Quality Control Board, Los Angeles Region 4 (RWQCB), California Santa Monica Mountains Conservancy (SMMC), California State Coastal Conservancy (SCC), California State Lands Commission (SLC), Colorado River Board, Office of Historic Preservation, San Gabriel and Lower Los Angeles Rivers and Mountains Conservancy (RMC), State Water Resources Control Board, Division of Drinking Water, State Water Resources Control Board, Division of Drinking Water, District 15, State Water Resources Control Board, Division of Drinking Water, District 16, State Water Resources Control Board, Division of Drinking Water, District 22, State Water Resources Control Board, Division of Drinking Water, District 7, State Water Resources Control Board, Division of Water Quality, State Water Resources Control Board, Division of Water Rights, State Water Resources Control Board, Division of Financial Assistance, California Department of Transportation, District 7 (DOT)
<b>State Reviewing Agency Comments</b>	California Department of Transportation, District 7 (DOT)
<b>Development Types</b>	Water Facilities (Stormwater)(Type Stormwater, MGD 1)
<b>Local Actions</b>	Site Plan, Stormwater Project
<b>Project Issues</b>	Aesthetics, Agriculture and Forestry Resources, Air Quality, Biological Resources, Cultural Resources, Drainage/Absorption, Flood Plain/Flooding, Geology/Soils, Growth Inducement, Hazards & Hazardous Materials, Hydrology/Water Quality, Land Use/Planning, Mineral Resources, Noise, Population/Housing, Public Services, Recreation, Schools/Universities, Septic System, Sewer Capacity, Solid Waste, Transportation, Vegetation, Wetland/Riparian, Wildfire
<b>Public Review Period Start</b>	5/27/2025
<b>Public Review Period End</b>	6/25/2025

## Accomplishments

### Zamora Park Renovation Project



**Owner:** City of El Monte  
**Construction Start:** 4/2025  
**Construction Completion:** 1/2026  
**Project Phase:** Construction



#### Project Updates

- **March 10, 2025** – Ground-Breaking Event
- **April 7, 2025** – Construction Began



#### Project Highlights

- The project plans to capture and infiltrate stormwater at an average rate of 0.23-acre feet per year using green infrastructure and Low Impact Development components. In addition, several park amenities will be added or renovated in the 4.48-acre park.



## Accomplishments

### Fairplex



**Owner:** East San Gabriel Valley Watershed Management Group  
**Construction Start:** 9/1/2026  
**Construction Completion:** 9/3/2029  
**Project Phase:** Design



### Community Engagement Events

- **February 20, 2025** – Community Outreach Event



### Project Highlights

- This project aims to capture urban runoff from the San Jose Creek Channel, treat the diverted flow, and infiltrate the treated water in a subsurface storage system.



**RESCHEDULED**  
DUE TO EXTREME WEATHER ADVISORY  
**NEW DATE: 2/20/2025 AT 6PM**  
Zoom Option Available: <https://bit.ly/fairplexSCWP>

**FAIRPLEX DRAIN STORMWATER CAPTURE AT GANESHA PARK PROJECT**

Join us for our outreach meeting!

When and where:  
**NEW DATE**  
Thursday, February 20th at 6:00pm  
Ganesha Park Community Center  
1575 N White Ave, Pomona, CA 91768



## Critical Issues

PROJECT NAME	ACTIVITY DELAYS / CONCERNS
Bassett High School Stormwater Capture Multi-Benefit Project	CEQA Not Started
Barnes Park	Schedule Delay
Encanto Park Stormwater Capture Project	MND In Progress/Completed
Glendora Avenue Green Streets	Schedule Delay
Pelota Park	Schedule Delay

Questions?





# Thank you

QUESTIONS?

Contact:

Uriel Cobian, PE ([SafeCleanWaterLA@pw.lacounty.gov](mailto:SafeCleanWaterLA@pw.lacounty.gov) & [ucobian@dpw.lacounty.gov](mailto:ucobian@dpw.lacounty.gov))

For inquiries related to reporting, [SCWPReporting@hdrinc.com](mailto:SCWPReporting@hdrinc.com)

For other inquires, [SafeCleanWaterLA@pw.lacounty.gov](mailto:SafeCleanWaterLA@pw.lacounty.gov)
