



**SAFE CLEAN
WATER PROGRAM**

Regional Program FY25-26 Mid-Year Report Summary

SAFE CLEAN WATER PROGRAM

August 18, 2026

RIO HONDO (RH)



Reporting Requirements

Infrastructure Project Developers and Scientific Study Developers are required to prepare Mid-Year (previously Quarterly) and Annual Progress/Expenditure Reports.

Reports are submitted to their respective Watershed Area Steering Committee to be evaluated on **whether the schedules, budget, scopes, and expected benefits have significantly changed or remain consistent** with the Safe, Clean Water Program goals.


Safe Clean Water Reporting Module



[Click Here! ↑](#)

The Reporting Repository houses:

- Regional Program Infrastructure Project/Scientific Studies Applications and completed Reports
- Completed Municipal Program Annual Plans and Reports
- SCW Program Reports



Reporting Repository

Reporting is an essential element of the Safe, Clean Water Program (SCWP) to track progress, quantify benefits, account for expenditures, and ensure transparency. Explore the Reporting Repository to learn about SCWP progress and access reports and plans for the Regional and Municipal Programs.

For more details on each of the report types available below and the SCWP Reporting timeline please visit the [Reporting and Audits](#) informational page.

Regional Program | Municipal Program

Lower Los Angeles River | Category | Quarterly Report | Name | Q4 (April - June) | FY23-24 | Clear All Filters

Use dropdowns above to filter this table:

Watershed Area	Category	Document Type	Name	Report Period	Fiscal Year	Downloads
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Urban Orchard Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Lynwood City Park Stormwater Capture Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River, Lower San Gabriel River	Scientific Study (SS)	Quarterly Report	Gateway Area Pathfinding Analysis (GAP Analysis) - Phase 2	Q4 (April - June)	FY23-24	Download

Recent and Upcoming Project Developer Deadlines

PROJECT DEVELOPER REPORT	REPORTING PERIOD	DUE DATE	WASC REVIEW
FY25-26 Mid-Year	July 2025 – December 2025	Feb 15, 2026	Spring/Summer 2026
FY25-26 Annual Report	July 2025 – June 2026	Aug 15, 2026	Winter 2026/2027
FY26-27 Mid-Year	July 2026 – December 2026	Feb 15, 2027	Spring/Summer 2027
FY26-27 Annual Report	July 2026 – June 2027	Aug 15, 2027	Winter 2027/2028

WASC Role in reviewing Progress/Expenditure Reports

Progress/Expenditure Reports

- WASCs are responsible for reviewing progress/expenditure reports submitted by Developers for funded Projects/Scientific Studies to evaluate:
 - Changes in schedules, scopes, expected benefits
 - If efforts remain consistent with SCW Program Goals
- Developers are requested to attend WASC meetings to describe the current project status and respond to questions about reported activities

This reporting period summary covers **July 1, 2025 to December 31, 2025** for Projects and Scientific Studies approved in FY20-21 through FY24-25 Stormwater Investment Plans.

WASC Funding Overview as of 12/31/2025

Reporting Period FY25-26:

Regional reports due 45 days
after end of reporting period. 

- **Mid-Year Reporting Period**
July 1, 2025 – December 31, 2025

Total Anticipated SCW Funding

\$77,500,641

Total Funds Awarded to Date

\$58,146,527

Total Funds Received to Date

\$30,217,134

Total Reported Expenditures To Date

\$16,840,918

WASC Funding Overview as of 12/31/2025

WASC Funding Definitions:

- **Total Anticipated SCW Funding:** Total SCW Funding Budgeted and Projected in FY20-21 through FY25-26 Stormwater Investment Plans (SIPs).
- **Total Funds Awarded to Date:** Total budgeted in FY20-21 through FY25-26 SIPs. This is the maximum amount that a Project/Scientific Study Developer may have received at the time of submitting FY25-26 Mid-Year Reports.
- **Total Funds Received to Date:** Total budgeted funds that the Project or Scientific Study has received through the execution of the Funds Transfer Agreement(s).
- **Total Reported Expenditures:** The total amount of expenditures reported by the Project/Scientific Study Developer as of 12/31/2025.

WASC Funding Overview as of 12/31/2025

(Slide 1 of 5)

PROJECT OR SCIENTIFIC STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Additional Funding Request to Support the LRS Adaptation Addressing the LA River Bacteria TMDL for the ULAR Watershed Management Group (RH)	FY22-23	\$115,029	\$115,029	\$115,029	\$114,774
Alhambra Wash Dry- Weather Diversion	FY21-22	\$2,572,180	\$2,572,180	\$275,300	\$0
Baldwin Lake and Tule Pond Restoration Project	FY20-21	\$8,500,000	\$8,500,000	\$8,500,000	\$708,530
Burke Heritage Park & Marengo Yard Stormwater Capture Project	FY23-24	\$4,424,118	\$4,424,118	\$787,896	\$579,657
East Los Angeles College Northeast Drainage Area and City of Monterey Park Biofiltration Project	FY21-22	\$1,032,618	\$1,032,618	\$60,524	\$211,235

WASC Funding Overview as of 12/31/2025

(Slide 2 of 5)

PROJECT OR SCIENTIFIC STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
East Los Angeles Sustainable Median Stormwater Capture Project ¹	FY20-21	\$7,000,000	\$7,000,000	\$7,000,000	\$7,000,000
Eaton Wash Dry-Weather Diversion	FY21-22	\$1,729,220	\$1,729,220	\$247,000	\$0
El Monte Norwood Elementary School Stormwater Capture Project	FY23-24	\$9,828,559	\$4,158,237	\$0	\$0
Fire Effects Study in the ULAR Watershed Management Area (RH)	FY21-22	\$281,112	\$281,112	\$281,112	\$226,908
Identifying Best Practices for Maintaining Stormwater Drywell Capacity (RH)	FY24-25	\$408,871	\$161,170	\$79,989	\$28,850

¹This project has been completed.

WASC Funding Overview as of 12/31/2025

(Slide 3 of 5)

PROJECT OR SCIENTIFIC STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Kinneloa Yard Stormwater Capture Project Preliminary Design and Feasibility Study ¹	FY23-24	\$2,292,762	\$2,292,762	\$2,292,762	\$1,844,653
LRS Adaptation to Address the LA River Bacteria TMDL for the ULAR Watershed Management Group (RH) ²	FY20-21	\$264,500	\$264,500	\$264,500	\$264,500
Maximizing Impact of Minimum Control Measures (RH)	FY22-23	\$240,466	\$240,466	\$240,466	\$238,655

¹The project name changed from “Kinneloa Yard Stormwater Capture Project Preliminary Design and Feasibility Study” to “Eaton Wash Stormwater Capture Project”.

²This project has been completed.

WASC Funding Overview as of 12/31/2025

(Slide 4 of 5)

PROJECT OR SCIENTIFIC STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Merced Ave Greenway (Phase I - South Residential Corridor)	FY21-22	\$3,234,694	\$3,234,694	\$3,197,240	\$2,871,618
Merced Avenue Stormwater Capture Project	FY23-24	\$9,799,210	\$6,895,493	\$1,068,059	\$452,733
Mt. Lowe Median Stormwater Capture Project	FY21-22	\$800,000	\$800,000	\$0	\$100,000
Plymouth School Neighborhood Stormwater Capture Demonstration Project ¹	FY21-22	\$559,162	\$559,162	\$548,662	\$569,179
preSIP: A Platform for Watershed Science and Project Collaboration (RH)	FY20-21	\$591,030	\$574,020	\$574,020	\$556,190

¹This project has been completed.

WASC Funding Overview as of 12/31/2025

(Slide 5 of 5)

PROJECT OR SCIENTIFIC STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Regional Pathogen Reduction Study (RH)	FY23-24	\$693,584	\$425,791	\$0	\$0
Rio Hondo Ecosystem Restoration Project	FY21-22	\$2,329,375	\$2,329,375	\$2,329,375	\$1,072,972
Rubio Wash Dry-Weather Diversion	FY21-22	\$2,812,080	\$2,812,080	\$241,800	\$0
South El Monte High School Stormwater Improvement Project ¹	FY24-25	\$1,264,800	\$1,264,800	\$0	\$0
Vincent Lugo Park Stormwater Capture Project	FY22-23	\$4,078,000	\$4,078,000	\$0	\$0
Washington Park Stormwater Capture Project	FY24-25	\$12,649,271	\$2,401,700	\$2,113,400	\$464

¹This project has been withdrawn by the Project Developer.

FY25-26 – Mid-Year Report Status

Number of Infrastructure Projects (IP)

INFRASTRUCTURE PROJECT REPORT STATUS	NUMBER OF PROJECTS
Concluded Project	0
Completed	16
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
TOTAL	16

Number of Scientific Studies (SS)

SCIENTIFIC STUDIES REPORT STATUS	NUMBER OF SCIENTIFIC STUDIES
Concluded Scientific Study	1
Completed	6
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
TOTAL	7

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 1 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATION & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Alhambra Wash Dry-Weather Diversion	X				
Baldwin Lake and Tule Pond Restoration Project	X				
Burke Heritage Park & Marengo Yard Stormwater Capture Project	X				
East Los Angeles College Northeast Drainage Area and City of Monterey Park Biofiltration Project	X				
East Los Angeles Sustainable Median Stormwater Capture Project				X	

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 2 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATION & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Eaton Wash Dry-Weather Diversion	X				
El Monte Norwood Elementary School Stormwater Capture Project	X				
Kinneloa Yard Stormwater Capture Project Preliminary Design and Feasibility Study	X				
Merced Ave Greenway (Phase I - South Residential Corridor)			X		
Merced Avenue Stormwater Capture Project	X				

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 3 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATION & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Mt. Lowe Median Stormwater Capture Project	X				
Plymouth School Neighborhood Stormwater Capture Demonstration Project				X	
Rio Hondo Ecosystem Restoration Project	X				
Rubio Wash Dry-Weather Diversion	X				
Vincent Lugo Park Stormwater Capture Project	X				
Washington Park Stormwater Project	X				

List of Infrastructure Program Projects and Scientific Studies Completed as of 12/31/2025

PROJECT OR SCIENTIFIC STUDY NAME	PROJECT TYPE
East Los Angeles Sustainable Median Stormwater Capture Project	Infrastructure Project
LRS Adaptation to Address the LA River Bacteria TMDL for the ULAR Watershed Management Group (RH)	Scientific Study
Plymouth School Neighborhood Stormwater Capture Demonstration Project	Infrastructure Project

Accomplishments

Additional Funding Request to Support the LRS Adaptation Addressing the LA River Bacteria TMDL for the ULAR Watershed Management Group



Owner: San Gabriel Valley Council of Governments

SS Start: 6/1/2023

SS Completion: 10/31/2025

SS Phase: Preparation of Reports




SS Updates

- Finalized Online Story Map updates including final Human Waste Source Investigation data



SS Highlights

- The Load Reduction Study (LRS) addresses the LA River Bacteria Total Maximum Daily Load (TMDL) and provides data to streamline the elimination of human waste sources from entering the storm drainage system.

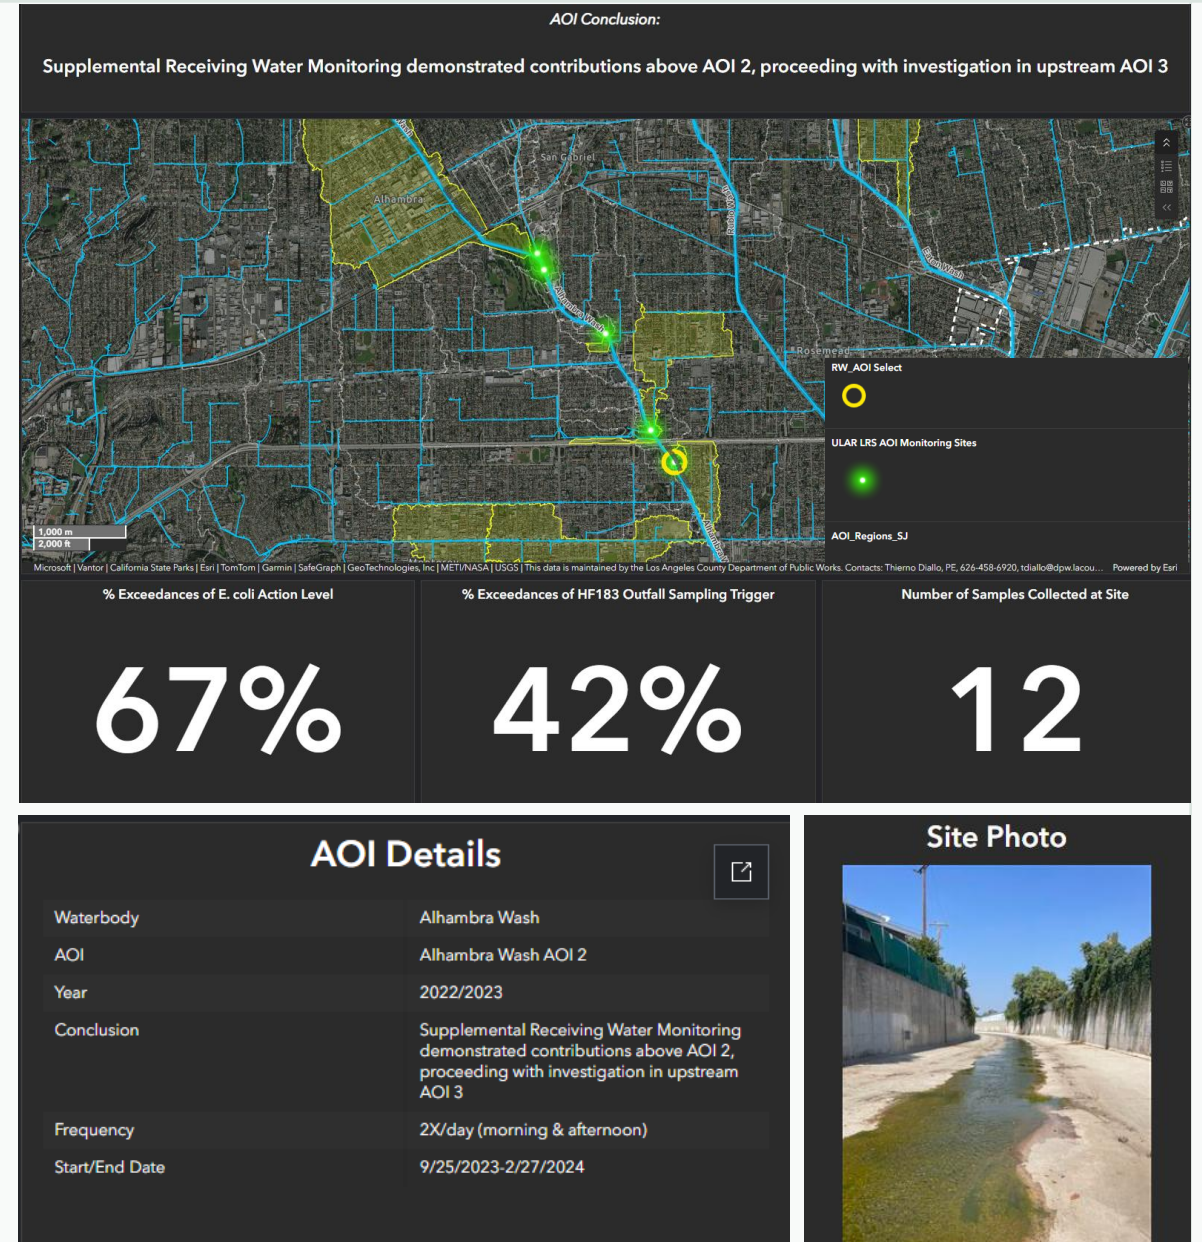

Accomplishments

Rio Hondo Ecosystem Restoration Project



Owner: City of Monrovia

Construction Start: 7/8/2030

Construction Completion: 7/7/2033

Project Phase: Design



Community Engagement Events

- **June 1, 2025 & December 13, 2025** - Community Outreach Events



Project Highlights

- This project was initiated to improve the water quality within the Rio Hondo River via stormwater capture, diversion, filtration, and storage.



RIO HONDO ECOSYSTEM RESTORATION PROJECT WORKSHOP

Join us for a community workshop to learn about the Rio Hondo Ecosystem Restoration Project. This stormwater capture project will help clean local water, while also making improvements to Peck Road Water Conservation Park.

June 1, 2025 | **9 AM - 12 PM** | **PECK ROAD WATER CONSERVATION PARK | 5401 PECK RD, ARCADIA, CA**

Want to ride to the workshop? Join us for a bike ride from Jeff Seymour Family Center! **RSVP: RioHondoProject.org**

Logos: City of Monrovia, Safe Clean Water Program, Arcadia, Craftwater

Illustration of three people riding bicycles on a path.

Informational Booth @ Peck Road Water Conservation Park

Peck Road Water Conservation Park
5401 Peck Road Arcadia, CA 91006

November 22, 2025 | 1 PM - 4 PM (Drop
by anytime!)

This is your opportunity to delve into the project's vision and, most importantly, share your valuable feedback and public comments.

Community Bike Ride from Jeff Seymour Family Center

Jeff Seymour Family Center
10900 Mulhall St, El Monte, CA 91731

December 13, 2025 | 9 AM - 12 PM

Join us for a community bike ride to Peck Road Water Conservation Park to learn about the exciting Rio Hondo Ecosystem Restoration Project!

RSVP

Informational Booth @ Peck Road Water Conservation Park

Peck Road Water Conservation Park
5401 Peck Road Arcadia, CA 91006

December 13, 2025 | 9 AM - 12 PM (Drop
by anytime!)

This is your opportunity to delve into the project's vision and, most importantly, share your valuable feedback and public comments. goes here

Critical Issues

(Slide 1 of 1)

PROJECT NAME	ACTIVITY DELAYS / CONCERNS
Alhambra Wash Dry-Weather Diversion	CEQA In Progress
Baldwin Lake and Tule Pond Restoration Project	CEQA In Progress
East Los Angeles College Northeast Drainage Area and City of Monterey Park Biofiltration Project	CEQA In Progress
Eaton Wash Dry-Weather Diversion	CEQA In Progress
Merced Avenue Stormwater Capture Project	CEQA In Progress
Mt. Lowe Median Stormwater Capture Project	CEQA In Progress Schedule Delay
Rubio Wash Dry-Weather Diversion	CEQA In Progress
Vincent Lugo Park Stormwater Capture Project	Schedule Delay

Questions?





Thank you

QUESTIONS?

Contact:

For inquiries related to reporting, SCWPReporting@hdrinc.com

For other inquiries, SafeCleanWaterLA@pw.lacounty.gov
