



Regional Program FY25-26 Mid-Year Report Summary

SAFE CLEAN WATER PROGRAM

August 19, 2026

SOUTH SANTA MONICA BAY (SSMB)



Reporting Requirements

Infrastructure Project Developers and Scientific Study Developers are required to prepare Mid-Year (previously Quarterly) and Annual Progress/Expenditure Reports.

Reports are submitted to their respective Watershed Area Steering Committee to be evaluated on **whether the schedules, budget, scopes, and expected benefits have significantly changed or remain consistent** with the Safe, Clean Water Program goals.


Safe Clean Water Reporting Module



[Click Here! ↑](#)

The Reporting Repository houses:

- Regional Program Infrastructure Project/Scientific Studies Applications and completed Reports
- Completed Municipal Program Annual Plans and Reports
- SCW Program Reports



Reporting Repository

Reporting is an essential element of the Safe, Clean Water Program (SCWP) to track progress, quantify benefits, account for expenditures, and ensure transparency. Explore the Reporting Repository to learn about SCWP progress and access reports and plans for the Regional and Municipal Programs.

For more details on each of the report types available below and the SCWP Reporting timeline please visit the [Reporting and Audits](#) informational page.

Regional Program | Municipal Program

Lower Los Angeles River % | Category | Quarterly Report % | Name | Q4 (April - June) % | FY23-24 % | Clear All Filters

Use dropdowns above to filter this table:

< 1 >

Watershed Area	Category	Document Type	Name	Report Period	Fiscal Year	Downloads
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Urban Orchard Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Lynwood City Park Stormwater Capture Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River, Lower San Gabriel River	Scientific Study (SS)	Quarterly Report	Gateway Area Pathfinding Analysis (GAP Analysis) - Phase 2	Q4 (April - June)	FY23-24	Download

Recent and Upcoming Project Developer Deadlines

PROJECT DEVELOPER REPORT	REPORTING PERIOD	DUE DATE	WASC REVIEW
FY25-26 Mid-Year	July 2025 – December 2025	Feb 15, 2026	Spring/Summer 2026
FY25-26 Annual Report	July 2025 – June 2026	Aug 15, 2026	Winter 2026/2027
FY26-27 Mid-Year	July 2026 – December 2026	Feb 15, 2027	Spring/Summer 2027
FY26-27 Annual Report	July 2026 – June 2027	Aug 15, 2027	Winter 2027/2028

WASC Role in reviewing Progress/Expenditure Reports

Progress/Expenditure Reports

- WASCs are responsible for reviewing progress/expenditure reports submitted by Developers for funded Projects/ Studies to evaluate:
 - Changes in schedules, scopes, expected benefits
 - If efforts remain consistent with SCW Program Goals
- Developers are requested to attend WASC meetings to describe the current project status and respond to questions about reported activities

This reporting period summary covers **July 1, 2025 to December 31, 2025** for Projects and Studies approved in FY20-21 through FY24-25 Stormwater Investment Plans

WASC Funding Overview as of 12/31/2025

Reporting Period FY25-26:

Regional reports due 45 days
after end of reporting period. 

- **Annual Reporting Period**
July 1, 2025 – December 31, 2025

Total Anticipated SCW Funding

\$125,977,066

Total Funds Awarded to Date

\$95,229,500

Total Funds Received to Date

\$56,785,596

Total Reported Expenditures To Date

\$40,702,238

WASC Funding Overview as of 12/31/2025

WASC Funding Definitions:

- **Total Anticipated SCW Funding:** Total SCW Funding Budgeted and Projected in FY20-21 through FY25-26 Stormwater Investment Plans (SIPs).
- **Total Funds Awarded to Date:** Total budgeted in FY20-21 through FY25-26 SIPs. This is the maximum amount that a Project Developer may have received at the time of submitting FY25-26 Mid-Year Reports.
- **Total Funds Received to Date:** Total budgeted funds that the Project or Scientific Study has received through the execution of the Funds Transfer Agreement(s).
- **Total Reported Expenditures:** The total amount of expenditures reported by the Project/Scientific Study Developer as of 12/31/2025.

WASC Funding Overview as of 12/31/2025

(Slide 1 of 3)

PROJECT OR SCIENTIFIC STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Alondra Park Multi Benefit Stormwater Capture Project	FY20-21	\$30,000,000	\$30,000,000	\$30,000,000	\$27,841,367
Beach Cities Green Streets Project	FY23-24	\$5,366,953	\$5,366,953	\$5,366,953	\$2,808,481
Carson Stormwater and Runoff Capture Project at Carriage Crest Park	FY21-22	\$1,037,500	\$1,037,500	\$207,500	\$0
Downtown Lomita Multi- Benefit Stormwater Project	FY22-23	\$449,300	\$449,300	\$449,300	\$449,300
Fulton Playfield Multi- Benefit Infiltration Project	FY22-23	\$8,302,138	\$6,349,000	\$2,166,000	\$367,744
Glen Anderson Park Regional Stormwater Capture Green Streets	FY23-24	\$782,000	\$782,000	\$782,000	\$226,572
Identifying Best Practices for Maintaining Stormwater Drywell Capacity (SSMB)	FY24-25	\$408,871	\$161,170	\$27,540	\$161,170

WASC Funding Overview as of 12/31/2025

(Slide 2 of 3)

PROJECT OR SCIENTIFIC STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Machado Lake Ecosystem Rehabilitation (MLER) Operations and Maintenance	FY23-24	\$3,199,371	\$1,805,866	\$1,805,866	\$0
Microplastics in LA County Stormwater (SSMB)	FY22-23	\$247,752	\$247,752	\$247,752	\$149,962
Recalculation of Wet Weather Zinc Criterion (SSMB)	FY20-21	\$57,886	\$57,886	\$57,886	\$52,713
Regional Pathogen Reduction Study (SSMB)	FY23-24	\$1,109,563	\$1,109,563	\$0	\$0
South Santa Monica Bay Water Quality Enhancement: 28th Street Storm Drain Infiltration Project	FY21-22	\$17,620,030	\$17,620,030	\$1,497,100	\$1,334,772
Stormwater Basin Expansion Project	FY21-22	\$4,505,000	\$4,505,000	\$4,505,000	\$4,302,743

WASC Funding Overview as of 12/31/2025

(Slide 3 of 3)

PROJECT OR SCIENTIFIC STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Street Sweeping Study (SSMB)	FY24-25	\$113,100	\$99,180	\$0	\$0
Torrance Airport Storm Water Basin Project	FY24-25	\$19,190,402	\$2,950,000	\$0	\$0
Torrance Airport Storm Water Basin Project, Phase 2	FY20-21	\$906,000	\$906,000	\$906,000	\$790,992
West Rancho Dominguez - San Pedro Street Green Improvement	FY22-23	\$800,000	\$800,000	\$800,000	\$0
Wilmington Neighborhood Greening Project	FY21-22	\$16,683,000	\$14,183,000	\$1,167,400	\$1,161,816
Wilmington Q Street Local Urban Area Flow Management Project	FY20-21	\$4,923,700	\$4,923,700	\$4,923,700	\$900,667
Wilmington-Anaheim Green Infrastructure Corridor Project	FY23-24	\$10,274,500	\$1,875,600	\$1,875,600	\$153,940

FY25-26 – Mid-Year Report Status



Number of Infrastructure Projects (IP)

INFRASTRUCTURE PROJECT REPORT STATUS	NUMBER OF PROJECTS
Concluded Project	0
Completed	14
In Progress / Pending	1
Incomplete / Missing	0
N/A	0
TOTAL	15



Number of Scientific Studies (SS)

SCIENTIFIC STUDIES REPORT STATUS	NUMBER OF STUDIES
Concluded Scientific Study	1
Completed	4
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
TOTAL	5

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 1 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Alondra Park Multi Benefit Stormwater Capture Project			X		
Beach Cities Green Streets Project			X		
Carson Stormwater and Runoff Capture Project at Carriage Crest Park			X		
Downtown Lomita Multi-Benefit Stormwater Project	X				
Fulton Playfield Multi-Benefit Infiltration Project	X				
Glen Anderson Park Regional Stormwater Capture Green Streets	X				

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 2 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST- CONSTRUCTION MONITORING
Machado Lake Ecosystem Rehabilitation (MLER) Operations and Maintenance				X	
South Santa Monica Bay Water Quality Enhancement: 28th Street Storm Drain Infiltration Project		X			
Stormwater Basin Expansion Project					X
Torrance Airport Storm Water Basin Project	X				

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 3 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST- CONSTRUCTION MONITORING
Torrance Airport Storm Water Basin Project, Phase 2	X				
West Rancho Dominguez - San Pedro Street Green Improvement	X				
Wilmington Neighborhood Greening Project	X				
Wilmington Q Street Local Urban Area Flow Management Project	X				
Wilmington-Anaheim Green Infrastructure Corridor Project	X				

List of Infrastructure Program Projects and Scientific Studies Completed as of 12/31/2025

PROJECT OR SCIENTIFIC STUDY NAME	PROJECT TYPE
Recalculation of Wet Weather Zinc Criterion	Scientific Study

Accomplishments

Fulton Playfield Multi-Benefit Infiltration Project



Owner: City of Redondo Beach
Construction Start: 5/1/2026
Construction Completion: 7/1/2027
Project Phase: Design




Project Updates

- Completed CEQA Process
- Progressed with detailed design and LACFCD permit coordination



Project Highlights

- This project plans to improve water quality by diverting, treating, and infiltrating stormwater before it reaches the Santa Monica Bay.

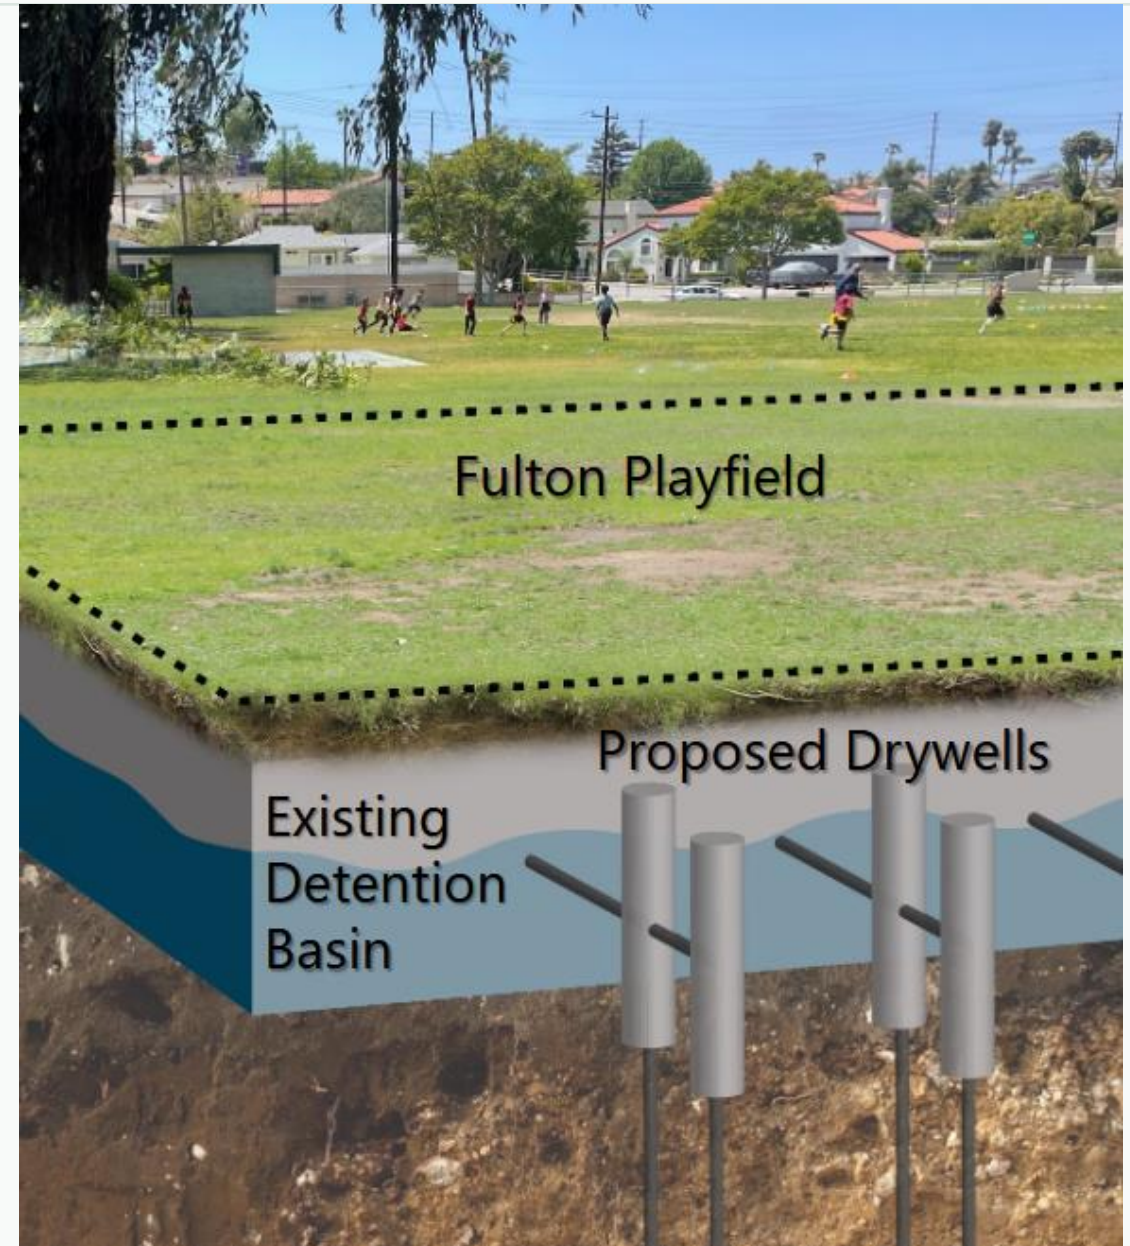

Accomplishments

South Santa Monica Bay Water Quality Enhancement: 28th Street Storm Drain Infiltration Project



Owner: City of Manhattan Beach (Mamerto Estepa Jr., Prem Kumar, and Shawn Igoe)

Construction Start: 9/1/2021

Construction Completion: 3/30/2027

Project Phase: Bid/Award



Project Updates

- October 23, 2025 – City presented Traffic Control Plan to Public Parking Improvement Commission
- December 16, 2025 – City staff presented bid/award results during City Council Meeting



Project Highlights

- This project aims to divert, treat, and infiltrate storm drain runoff to improve water quality entering the ocean downstream.

City Council Regular Meeting

Regular Meeting

Tuesday, December 16, 2025

6:00 PM

City Council Chambers and Zoom



ELECTED OFFICIALS

Mayor David Lesser

Mayor Pro Tem Joe Franklin

Councilmember Nina Trieu Tamay

Councilmember Steve S. Charelian

Councilmember Amy Thomas Howorth

EXECUTIVE TEAM

City Manager Talyn Mirzakhanian

City Attorney Quinn Barrow

City Clerk Liza Tamura

Finance Director Libby Bretthauer

Human Resources Director Lisa Jenkins

Parks and Recreation Director Mark Leyman

Police Chief Rachel Johnson

Fire Chief Jesse Alexander

Community Development Director Masa Alkire

Interim Public Works Director Toufic Semaan

Information Technology Director Miguel Guardado

MISSION STATEMENT

Critical Issues

(Slide 1 of 1)

PROJECT NAME	ACTIVITY DELAYS / CONCERNS
Carson Stormwater and Runoff Capture Project at Carriage Crest Park	Schedule Delay
Fulton Playfield Multi-Benefit Infiltration Project	Schedule Delay
Glen Anderson Park Regional Stormwater Capture Green Streets	Schedule Delay
South Santa Monica Bay Water Quality Enhancement: 28 th Street Storm Drain Infiltration Project	Schedule Delay, CEQA In Progress
Stormwater Basin Expansion Project	Missing Post-Performance Report
West Rancho Dominguez – San Pedro Street Green Improvement	Planning Delay
Wilmington Neighborhood Greening Project	CEQA In Progress
Wilmington Q Street Local Urban Area Flow Management Project	Schedule Delay
Wilmington-Anaheim Green Infrastructure Corridor Project	Schedule Delay

Questions?





Thank you

QUESTIONS?

Contact:

Eric Bonilla, PE (SafeCleanWaterLA@pw.lacounty.gov & ebonilla@dpw.lacounty.gov)

For inquiries related to reporting, SCWPReporting@hdrinc.com

For other inquiries, SafeCleanWaterLA@pw.lacounty.gov
