



**SAFE CLEAN
WATER PROGRAM**

Regional Program FY25-26 Mid-Year Report Summary

SAFE CLEAN WATER PROGRAM
August 11, 2026
Lower San Gabriel River (LSGR)



Reporting Requirements

Infrastructure Project Developers and Scientific Study Developers are required to prepare Mid-Year (previously Quarterly) and Annual Progress/Expenditure Reports.

Reports are submitted to their respective Watershed Area Steering Committee to be evaluated on **whether the schedules, budget, scopes, and expected benefits have significantly changed or remain consistent** with the Safe, Clean Water Program goals.


Safe Clean Water Reporting Module



[Click Here! ↑](#)

The Reporting Repository houses:

- Regional Program Project/Scientific Studies Applications and completed Reports
- Completed Municipal Program Annual Plans and Reports
- SCW Program Reports

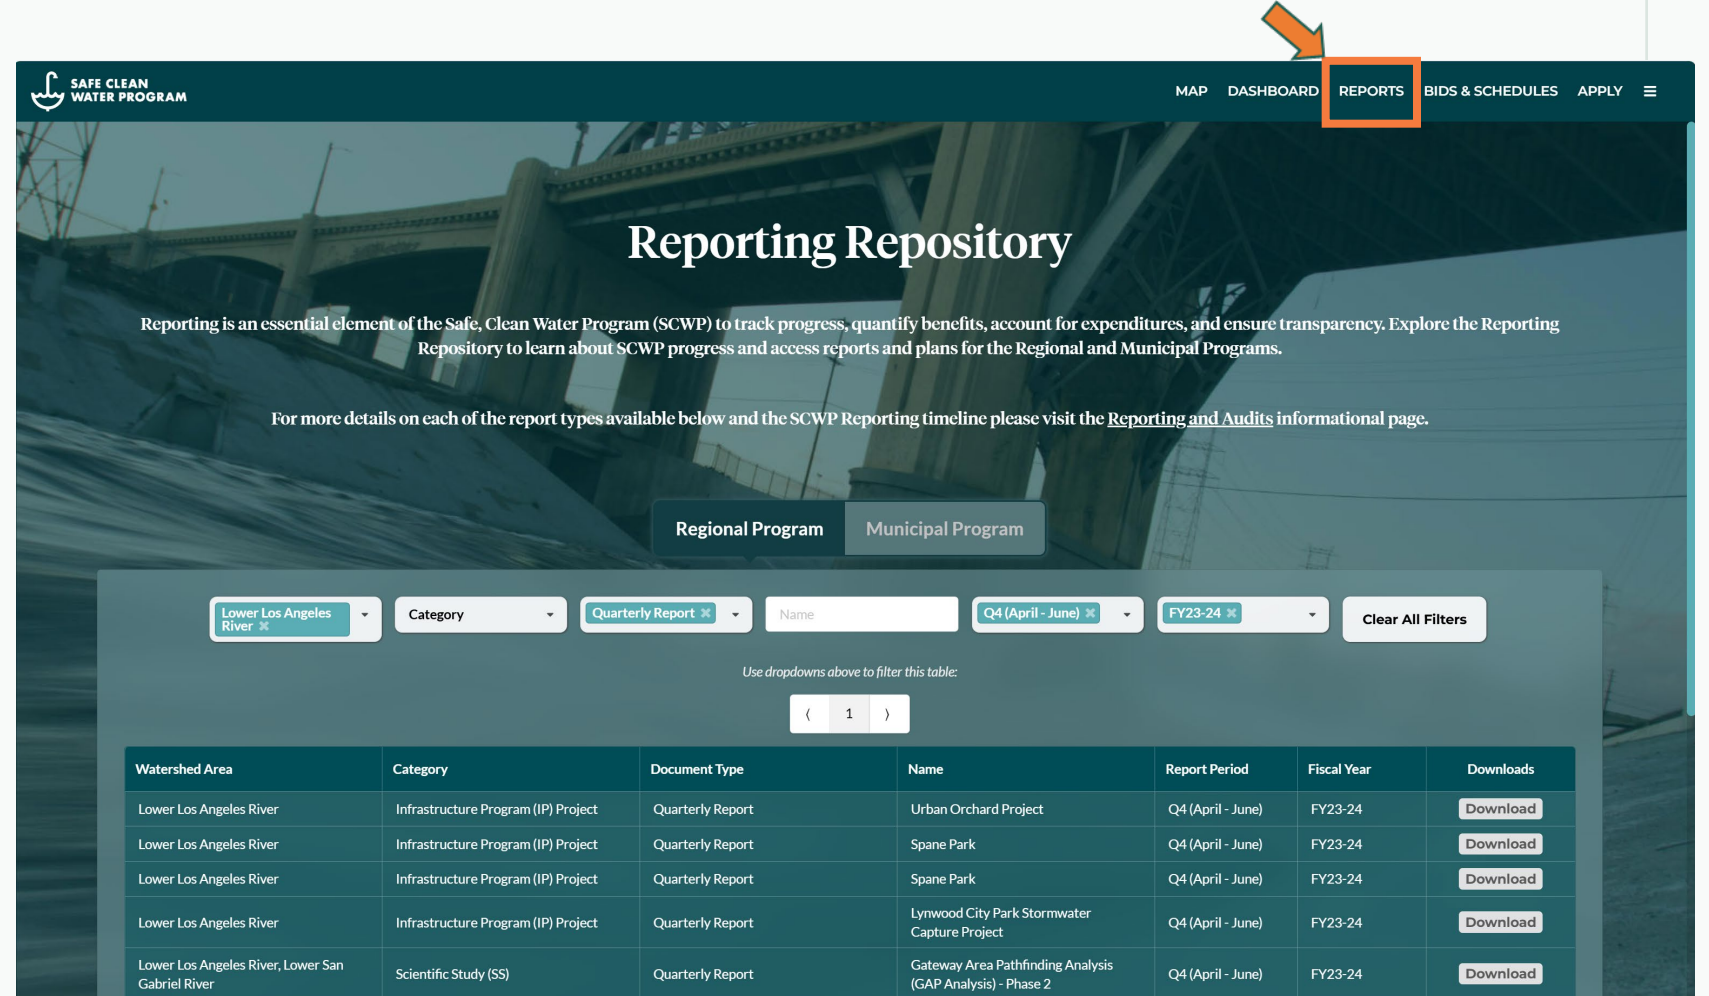

Reporting Repository

Reporting is an essential element of the Safe, Clean Water Program (SCWP) to track progress, quantify benefits, account for expenditures, and ensure transparency. Explore the Reporting Repository to learn about SCWP progress and access reports and plans for the Regional and Municipal Programs.

For more details on each of the report types available below and the SCWP Reporting timeline please visit the [Reporting and Audits](#) informational page.

Regional Program | Municipal Program

Lower Los Angeles River % | Category | Quarterly Report % | Name | Q4 (April - June) % | FY23-24 % | Clear All Filters

Use dropdowns above to filter this table:

< 1 >

Watershed Area	Category	Document Type	Name	Report Period	Fiscal Year	Downloads
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Urban Orchard Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Lynwood City Park Stormwater Capture Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River, Lower San Gabriel River	Scientific Study (SS)	Quarterly Report	Gateway Area Pathfinding Analysis (GAP Analysis) - Phase 2	Q4 (April - June)	FY23-24	Download

Recent and Upcoming Project Developer Deadlines

PROJECT DEVELOPER REPORT	REPORTING PERIOD	DUE DATE	WASC REVIEW
FY25-26 Mid-Year	July 2025 – December 2025	Feb 15, 2026	Spring/Summer 2026
FY25-26 Annual Report	July 2025 – June 2026	Aug 15, 2026	Winter 2026/2027
FY26-27 Mid-Year	July 2026 – December 2026	Feb 15, 2027	Spring/Summer 2027
FY26-27 Annual Report	July 2026 – June 2027	Aug 15, 2027	Winter 2027/2028

WASC Role in reviewing Progress/Expenditure Reports

Progress/Expenditure Reports

- WASCs are responsible for reviewing progress/expenditure reports submitted by Developers for funded Projects/Studies to evaluate:
 - Changes in schedules, scopes, expected benefits
 - If efforts remain consistent with SCW Program Goals
- Developers are requested to attend WASC meetings to describe the current project status and respond to questions about reported activities

This reporting period summary covers **July 1, 2025 to December 31, 2025** for Projects and Studies approved in FY20-21 through FY24-25 Stormwater Investment Plans

WASC Funding Overview as of 12/31/2025

Reporting Period FY25-26:

Regional reports due 45 days
after end of reporting period. 

- **Mid-Year Reporting Period**
July 1, 2025 - December 31, 2025

Total Anticipated SCW Funding

\$111,841,877

Total Funds Awarded to Date

\$94,085,449

Total Funds Received to Date

\$42,270,195

Total Reported Expenditures To Date:

\$24,332,177

WASC Funding Overview as of 12/31/2025

WASC Funding Definitions:

- **Total Anticipated SCW Funding:** Total SCW Funding Budgeted and Projected in FY20-21 through FY25-26 Stormwater Investment Plans (SIPs).
- **Total Funds Awarded to Date:** Total budgeted in FY20-21 through FY25-26 SIPs. This is the maximum amount that a Project Developer may have received at the time of submitting FY25-26 Mid-Year Reports.
- **Total Funds Received to Date:** Total budgeted funds that the Project or Study has received through the execution of the Funds Transfer Agreement(s).
- **Total Reported Expenditures:** The total amount of expenditures reported by the Project/Study Developer as of 12/31/2025.

WASC Funding Overview as of 12/31/2025

(Slide 1 of 6)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Adventure Park Multi Benefit Stormwater Capture Project	FY20-21	\$13,500,000	\$13,500,000	\$13,500,000	\$13,500,000
Artesia Park Urban Runoff Capture Project ¹	FY23-24	\$1,568,876	\$1,568,876	\$0	\$0
Bellflower Simms Park Stormwater Capture Project	FY21-22	\$2,141,987	\$2,141,987	\$2,141,987	\$1,298,299
Bellflower Simms Park Stormwater Capture Project (Construction)	FY22-23	\$13,666,701	\$13,666,701	\$2,635,561	\$0
Bolivar Park	FY20-21	\$1,265,900	\$1,265,900	\$1,265,900	\$741,180

¹This project has been withdrawn in this reporting period and will not require further reporting.

WASC Funding Overview as of 12/31/2025

(Slide 2 of 6)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Caruthers Park	FY20-21	\$855,000	\$855,000	\$855,000	\$249,686
Cerritos Sports Complex	FY21-22	\$2,408,000	\$2,408,000	\$2,408,000	\$0
El Dorado Regional Project	FY20-21	\$3,000,000	\$3,000,000	\$3,000,000	\$2,267,753
Gateway Area Pathfinding Analysis (GAP Analysis) (LSGR) ¹	FY21-22	\$75,000	\$75,000	\$75,000	\$74,833
Gateway Area Pathfinding Analysis (GAP Analysis) - Phase 2 (LSGR) ¹	FY22-23	\$230,000	\$230,000	\$230,000	\$227,325

¹This project has been completed.

WASC Funding Overview as of 12/31/2025

(Slide 3 of 6)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Heartwell Park at Clark Channel Stormwater Capture Project	FY24-25	\$2,864,472	\$2,864,472	\$0	\$0
Heartwell Park at Palo Verde Channel Stormwater Capture Project	FY23-24	\$3,313,865	\$3,313,865	\$0	\$0
Hermosillo Park	FY20-21	\$30,017,101	\$16,703,977	\$4,100,000	\$2,089,387
Identifying Best Practices for Maintaining Stormwater Drywell Capacity	FY24-25	\$408,871	\$161,170	\$79,989	\$36,544

WASC Funding Overview as of 12/31/2025

(Slide 4 of 6)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Independence Park Runoff Capture Project	FY24-25	\$1,310,458	\$1,310,458	\$0	\$0
La Habra Heights Stormwater Treatment and Reuse System The Park Hacienda Road ¹	FY23-24	\$705,348	\$705,348	\$0	\$0
La Mirada Creek Park Project ²	FY23-24	\$5,752,200	\$5,752,200	\$5,752,200	\$0
Mayfair Park	FY20-21	\$1,266,125	\$1,266,125	\$1,266,125	\$279,264
Microplastics in LA County Stormwater (LSGR)	FY22-23	\$247,752	\$247,752	\$247,752	\$154,444

¹ This project may be withdrawn from the Safe Clean Water Program (SCWP).

² This project will be withdrawn, and the SCWP is initiating the process to recover funds.

WASC Funding Overview as of 12/31/2025

(Slide 5 of 6)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Progress Park Stormwater Capture Project	FY23-24	\$2,161,744	\$2,161,744	\$0	\$0
Regional Pathogen Reduction Study (LSGR)	FY23-24	\$1,007,287	\$618,374	\$0	\$0
Reservoir Park Stormwater Capture Project	FY24-25	\$6,676,878	\$2,870,188	\$0	\$0
Skylinks Golf Course at Wardlow Stormwater Capture Project	FY20-21	\$13,433,000	\$13,433,000	\$1,047,369	\$2,176,872
Sorensen Park Multi-Benefit Stormwater Capture Project	FY24-25	\$1,616,592	\$1,616,592	\$1,616,592	\$0

WASC Funding Overview as of 12/31/2025

(Slide 6 of 6)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Targeted Human Waste Source Reduction Strategy to Address Bacteria-Related Compliance Objectives for the Los Cerritos Channel (LSGR)	FY23-24	\$475,000	\$475,000	\$175,000	\$163,928
York Field Stormwater Capture Project	FY22-23	\$1,873,720	\$1,873,720	\$1,873,720	\$1,072,662

FY25-26 – Mid-Year Report Status

Number of Infrastructure Projects (IP)

INFRASTRUCTURE PROJECT REPORT STATUS	NUMBER OF PROJECTS
Concluded Project	0
Completed	17
In Progress / Pending	1
Incomplete / Missing	1
N/A	0
TOTAL	19

Number of Scientific Studies (SS)

SCIENTIFIC STUDIES REPORT STATUS	NUMBER OF STUDIES
Concluded Study	1
Completed	5
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
TOTAL	6

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 1 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATION & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Adventure Park Multi Benefit Stormwater Capture Project				X	
Bellflower Simms Park Stormwater Capture Project	X				
Bellflower Simms Park Stormwater Capture Project (Construction)	X				
Bolivar Park				X	
Caruthers Park				X	
Cerritos Sports Complex	X				

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 2 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATION & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
El Dorado Regional Project	X				
Heartwell Park at Clark Channel Stormwater Capture Project	X				
Heartwell Park at Palo Verde Channel Stormwater Capture Project	X				
Hermosillo Park	X				
Independence Park Runoff Capture Project	X				

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 3 of 3)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATION & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Mayfair Park					X
Progress Park Stormwater Capture Project	X				
Reservoir Park Stormwater Capture Project	X				
Skylinks Golf Course at Wardlow Stormwater Capture Project	X				
Sorensen Park Multi-Benefit Stormwater Capture Project	X				
York Field Stormwater Capture Project	X				

List of Infrastructure Program Projects and Scientific Studies Completed as of 12/31/2025

PROJECT OR STUDY NAME	PROJECT TYPE
Adventure Park Multi Benefit Stormwater Capture Project	Infrastructure Project
Bolivar Park	Infrastructure Project
Caruthers Park	Infrastructure Project
Mayfair Park	Infrastructure Project
Gateway Area Pathfinding Analysis (GAP Analysis) – Phase 1	Scientific Study
Gateway Area Pathfinding Analysis (GAP Analysis) – Phase 2	Scientific Study

Accomplishments

Adventure Park Multi Benefit Stormwater Capture Project



Owner: County of Los Angeles

Construction Start: 10/04/2022

Construction Completion: 10/15/2025

Project Phase: O&M



Project Updates

- **2025** – Park was officially opened to public



Project Highlights

- The project intercepts runoff from the Sorenson Drain, filtering and storing up to 6.4 million gallons of stormwater underground to improve water quality, reduce flooding, and enhance water resiliency for the region.



Ribbon-Cutting



Rendering of Underground Storage

Accomplishments

Skylinks Golf Course at Wardlow Stormwater Capture Project



Owner: City of Long Beach

Construction Start: 1/18/2027

Construction Completion: 1/19/2029

Project Phase: Design



Project Updates

- **July 2025** – Notice of Determination was filed/approved for clearance and construction of the project



Project Highlights

- This project plans to improve water quality for the Los Cerritos Channel Watershed and Alamitos Bay Watershed Management Area by diverting, treating, and infiltrating runoff from the Los Cerritos Channel.



 Recent Postings
  About
  Contact Us
  Search
  Advanced Search

Skylinks Regional Stormwater Capture Project

2 Documents in Project

Summary

SCH Number	2024030575
Lead Agency	City of Long Beach
Document Title	Skylinks Regional Stormwater Capture Project
Document Type	NOD - Notice of Determination
Received	7/17/2025
Posted	7/17/2025
Document Description	NOD for Site Plan Review (SPR25-019) for the site clearance and construction of the Skylinks Regional Stormwater Capture Project located within the northeast portion of the Skylinks Golf Course in the City of Long Beach. The project serves to address stormwater quality for both the Los Cerritos Channel Watershed and Alamitos Bay Watershed Management Area. The project will treat both dry- and wet-weather runoff by diverting flows from Los Cerritos Channel into a subsurface infiltration basin with a capacity of six acre feet. A portion of these flows will be pumped to a 200,000-gallon vegetative pond where it will be treated through a filter system before returning to the channel. The Project will also incorporate walking trails, benches, native vegetation, and interpretive signage in the project area.

Critical Issues

PROJECT NAME	ACTIVITY DELAYS / CONCERNS
Bolivar Park	Missing Post-Performance Report
Caruthers Park	Missing Post-Performance Report
El Dorado Regional Project	Schedule Delay
Mayfair Park	Missing Post-Performance Report
Progress Park Stormwater Capture Project	Design Work Delay

Questions?





Thank you

QUESTIONS?

Contact:

Uriel Cobian, PE (SafeCleanWaterLA@pw.lacounty.gov & ucobian@dpw.lacounty.gov)

For inquiries related to reporting, SCWPReporting@hdrinc.com

For other inquiries, SafeCleanWaterLA@pw.lacounty.gov
