



Regional Program FY25-26 Mid-Year Report Summary

SAFE CLEAN WATER PROGRAM

September 1, 2026

CENTRAL SANTA MONICA BAY (CSMB)



Reporting Requirements

Infrastructure Project Developers and Scientific Study Developers are required to prepare Mid-Year (previously Quarterly) and Annual Progress/Expenditure Reports.

Reports are submitted to their respective Watershed Area Steering Committee to be evaluated on **whether the schedules, budget, scopes, and expected benefits have significantly changed or remain consistent** with the Safe, Clean Water Program goals.


Safe Clean Water Reporting Module



[Click Here! ↑](#)

The Reporting Repository houses:

- Regional Program Infrastructure Project/Scientific Studies Applications and completed Reports
- Completed Municipal Program Annual Plans and Reports
- SCW Program Reports

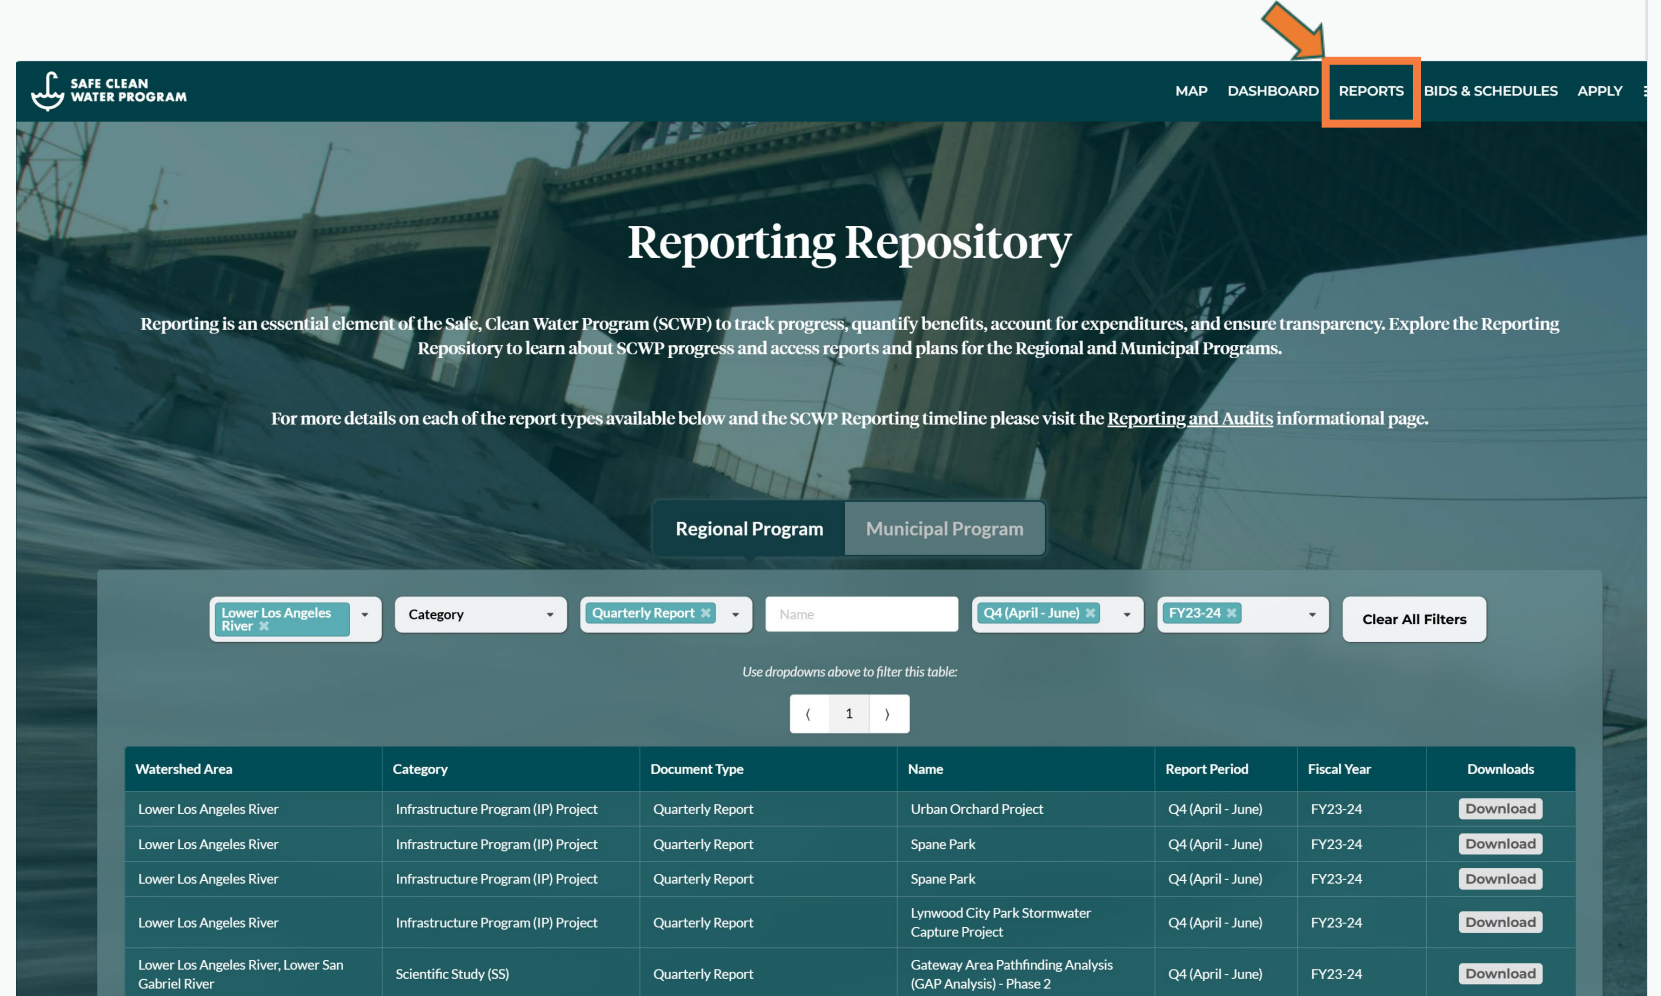

Reporting Repository

Reporting is an essential element of the Safe, Clean Water Program (SCWP) to track progress, quantify benefits, account for expenditures, and ensure transparency. Explore the Reporting Repository to learn about SCWP progress and access reports and plans for the Regional and Municipal Programs.

For more details on each of the report types available below and the SCWP Reporting timeline please visit the [Reporting and Audits](#) informational page.

Regional Program | Municipal Program

Lower Los Angeles River % | Category | Quarterly Report % | Name | Q4 (April - June) % | FY23-24 % | Clear All Filters

Use dropdowns above to filter this table:

< 1 >

Watershed Area	Category	Document Type	Name	Report Period	Fiscal Year	Downloads
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Urban Orchard Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Spane Park	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River	Infrastructure Program (IP) Project	Quarterly Report	Lynwood City Park Stormwater Capture Project	Q4 (April - June)	FY23-24	Download
Lower Los Angeles River, Lower San Gabriel River	Scientific Study (SS)	Quarterly Report	Gateway Area Pathfinding Analysis (GAP Analysis) - Phase 2	Q4 (April - June)	FY23-24	Download

Recent and Upcoming Project Developer Deadlines

PROJECT DEVELOPER REPORT	REPORTING PERIOD	DUE DATE	WASC REVIEW
FY25-26 Mid-Year	July 2025 – December 2025	Feb 15, 2026	Spring/Summer 2026
FY25-26 Annual Report	July 2025 – June 2026	Aug 15, 2026	Winter 2026/2027
FY26-27 Mid-Year	July 2026 – December 2026	Feb 15, 2027	Spring/Summer 2027
FY26-27 Annual Report	July 2026 – June 2027	Aug 15, 2027	Winter 2027/2028

WASC Role in reviewing Progress/Expenditure Reports

Progress/Expenditure Reports

- WASCs are responsible for reviewing progress/expenditure reports submitted by Developers for funded Projects/ Studies to evaluate:
 - Changes in schedules, scopes, expected benefits
 - If efforts remain consistent with SCW Program Goals
- Developers are requested to attend WASC meetings to describe the current project status and respond to questions about reported activities

This reporting period summary covers **July 1, 2025 to December 31, 2025** for Projects and Studies approved in FY20-21 through FY24-25 Stormwater Investment Plans

WASC Funding Overview as of 12/31/2025

Reporting Period FY25-26:

Regional reports due 45 days
after end of reporting period. 

- **Mid-Year Reporting Period**
July 1, 2025 – December 31, 2025

Total Anticipated SCW Funding

\$115,306,023

Total Funds Awarded to Date

\$96,239,770

Total Funds Received to Date

\$50,177,406

Total Reported Expenditures To Date

\$44,343,422

WASC Funding Overview as of 12/31/2025

WASC Funding Definitions:

- **Total Anticipated SCW Funding:** Total SCW Funding Budgeted and Projected in FY20-21 through FY25-26 Stormwater Investment Plans (SIPs).
- **Total Funds Awarded to Date:** Total budgeted in FY20-21 through FY25-26 SIPs. This is the maximum amount that a Project Developer may have received at the time of submitting FY25-26 Mid-Year Reports.
- **Total Funds Received to Date:** Total budgeted funds that the Project or Study has received through the execution of the Funds Transfer Agreement(s).
- **Total Reported Expenditures:** The total amount of expenditures reported by the Project/Study Developer as of 12/31/2025.

WASC Funding Overview as of 12/31/2025

(Slide 1 of 4)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Angeles Mesa Green Infrastructure Corridor Project	FY22-23	\$8,401,432	\$8,301,432	\$1,103,550	\$444,256
Baldwin Vista Green Streets Project	FY24-25	\$9,076,647	\$964,919	\$0	\$0
Ballona Creek TMDL Project	FY21-22	\$22,000,000	\$22,000,000	\$15,500,000	\$15,103,038
Beverly Hills Burton Way Green Street and Water Efficient Landscape Project	FY20-21	\$5,000,000	\$5,000,000	\$5,000,000	\$5,001,285
Community Garden Stormwater Capture Investigation (CSMB) ¹	FY22-23	\$378,284	\$378,284	\$378,284	\$144,562

¹This project has been completed and does not require submission of a progress report for this period.

WASC Funding Overview as of 12/31/2025

(Slide 2 of 4)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Culver City Mesmer Low Flow Diversion ¹	FY20-21	\$950,000	\$950,000	\$950,000	\$957,331
Edward Vincent Jr. Park Stormwater Improvements Project	FY22-23	\$4,270,000	\$4,270,000	\$3,645,000	\$3,040,280
Identifying Best Practices for Maintaining Stormwater Drywell Capacity (CSMB)	FY24-25	\$408,871	\$161,170	\$79,989	\$28,612
Imperial Highway Green Infrastructure Project	FY23-24	\$5,232,000	\$728,000	\$389,000	\$0
Ladera Heights - W Centinela Ave Green Improvement	FY22-23	\$500,000	\$500,000	\$500,000	\$0

¹This project has been completed.

WASC Funding Overview as of 12/31/2025

(Slide 3 of 4)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Ladera Park Stormwater Improvements Project ¹	FY20-21	\$2,000,000	\$2,000,000	\$2,000,000	\$2,000,000
MacArthur Lake Rehabilitation Project	FY20-21	\$31,043,718	\$28,043,718	\$4,000,000	\$4,179,984
Microplastics in LA County Stormwater (CSMB)	FY22-23	\$247,752	\$247,752	\$247,752	\$145,528
Monteith Park and View Park Green Alley Stormwater Improvements Project	FY20-21	\$4,550,000	\$4,550,000	\$4,550,000	\$4,550,000
Regional Pathogen Reduction Study (CSMB)	FY23-24	\$1,074,325	\$659,528	\$0	\$0

¹This project has been completed.

WASC Funding Overview as of 12/31/2025

(Slide 4 of 4)

PROJECT OR STUDY NAME	CALL FOR PROJECTS	ANTICIPATED SCW FUNDING	SCW FUNDS AWARDED TO DATE	SCW FUNDS RECEIVED TO DATE	REPORTED SCW EXPENDITURES TO DATE
Slauson Connect Clean Water Project	FY21-22	\$4,899,444	\$4,899,444	\$733,831	\$721,777
Street Sweeping Study	FY24-25	\$173,550	\$152,190	\$0	\$0
Sustainable Water Infrastructure Project ¹	FY20-21	\$7,500,000	\$7,500,000	\$7,500,000	\$7,500,000
Washington Boulevard Stormwater and Urban Runoff Diversion	FY20-21	\$7,600,000	\$4,933,333	\$3,600,000	\$526,769

¹This project has been completed.

FY25-26 – Mid-Year Report Status

Number of Infrastructure Projects (IP)

INFRASTRUCTURE PROJECT REPORT STATUS	NUMBER OF PROJECTS
Concluded Project	0
Completed	14
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
TOTAL	14

Number of Scientific Studies (SS)

SCIENTIFIC STUDIES REPORT STATUS	NUMBER OF STUDIES
Concluded Study	1
Completed	4
In Progress / Pending	0
Incomplete / Missing	0
N/A	0
TOTAL	5

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 1 of 4)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST- CONSTRUCTION MONITORING
Angeles Mesa Green Infrastructure Corridor Project	X				
Baldwin Vista Green Streets Project	X				
Ballona Creek TMDL Project			X		
Beverly Hills Burton Way Green Street and Water Efficient Landscape Project					X

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 2 of 4)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Culver City Mesmer Low Flow Diversion					X
Edward Vincent Jr. Park Stormwater Improvements Project	X				
Imperial Highway Green Infrastructure Project	X				
Ladera Heights - W Centinela Ave Green Improvement	X				

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 3 of 4)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST-CONSTRUCTION MONITORING
Ladera Park Stormwater Improvements Project				X	
MacArthur Lake Rehabilitation Project	X				
Monteith Park and View Park Green Alley Stormwater Improvements Project				X	
Slauson Connect Clean Water Project	X				

List of Infrastructure Program Projects by Phase as of 12/31/2025

(Slide 4 of 4)

PROJECT NAME	PLANNING / DESIGN	BID / AWARD	CONSTRUCTION	OPERATIONS & MAINTENANCE (O&M)	POST- CONSTRUCTION MONITORING
Sustainable Water Infrastructure Project				X	
Washington Boulevard Stormwater and Urban Runoff Diversion			X		

List of Infrastructure Program Projects and Scientific Studies Completed as of 12/31/2025

PROJECT OR STUDY NAME	PROJECT TYPE
Beverly Hills Burton Way Green Street and Water Efficient Landscape Project	Infrastructure Project
Culver City Mesmer Low Flow Diversion	Infrastructure Project
Ladera Park Stormwater Improvements Project	Infrastructure Project
Monteith Park and View Park Green Alley Stormwater Improvements Project	Infrastructure Project
Sustainable Water Infrastructure Project	Infrastructure Project
Community Garden Stormwater Capture Investigation	Scientific Study

Accomplishments

MacArthur Lake Rehabilitation Project



Owner: City of Los Angeles,
LA Sanitation and Environment
Construction Start: 8/1/2026
Construction Completion: 1/31/2029
Project Phase: Design



Project Updates

- **August 2025** – Completed Final EIR

Project Highlights



- The project aims to achieve water quality objectives for the Ballona Creek Watershed by diverting stormwater and dry weather flows from the existing storm drain system, treating the water, and discharging it into MacArthur Lake for storage or returning it to the storm drain system.



 Recent Postings
  About
  Contact Us
  Search

[Home](#) | [Search](#) | [SCH Number: 2022040153](#) | MacArthur Lake Stormwater Capture Project

MacArthur Lake Stormwater Capture Project

4 Documents in Project

Summary	
SCH Number	2022040153
Lead Agency	City of Los Angeles
Document Title	MacArthur Lake Stormwater Capture Project
Document Type	FIN - Final Document
Received	9/2/2025



State Clearinghouse No. 2022040153 | August 2025

Accomplishments

Monteith Park and View Park Green Alley Stormwater Improvements Project



Owner: County of Los Angeles

Construction Start: 6/7/2023

Construction Completion: 12/27/2025

Project Phase: O&M



Project Updates

- **12/27/2025** - Construction was completed



Project Highlights

- The project plans to improve water quality in the Ballona Creek and Santa Monica Bay by capturing, treating, and infiltrating collected stormwater runoff from 228 acres of residential and commercial land areas.



Permeable Pavement



Bioswale



Drywells

Critical Issues

(Slide 1 of 1)

PROJECT NAME	ACTIVITY DELAYS / CONCERNS
Angeles Mesa Green Infrastructure Corridor Project	CEQA In Progress Schedule Delay
Baldwin Vista Green Streets Project	Schedule Delay
MacArthur Lake Rehabilitation Project	CEQA In Progress
Slauson Connect Clean Water Project	CEQA In Progress
Sustainable Water Infrastructure Project	Concern/Delay with Third Year of Operations

Questions?





Thank you

QUESTIONS?

Contact:

Pablo Forni, PE (SafeCleanWaterLA@pw.lacounty.gov & pforni@dpw.lacounty.gov)

For inquiries related to reporting, SCWPReporting@hdrinc.com

For other inquiries, SafeCleanWaterLA@pw.lacounty.gov
