



SAFE CLEAN
WATER PROGRAM

Project Modification Requests

SAFE CLEAN WATER PROGRAM
2026



Project Modification Requests

- **Infrastructure Program (IP)** projects and **Scientific Studies (SS)** that were **previously approved** in SIPs are eligible for future funding, subject to approval in the pending SIP
 - Any proposed modifications to a continuing Project or Scientific Study shall be disclosed in a **Project Modification Request (PMR) form** and evaluated in accordance with the [Project Modification Guidelines](#)
- Once a Project or Scientific Study has been included in the SIP for a fiscal year and a Transfer Agreement or Addendum has been executed for that fiscal year, a Recipient that proposes modifications to the **schedule, scope, benefits, and/or funding amounts** of the Project or Scientific Study, should contact Public Works and submit a PMR form.

Project Modification Guidelines



- The Project Modification Guidelines provide more specific guidance when modifications to a project, project concept or scientific study are proposed during the course of a typical fiscal year
- The Project Modification Request (PMR) form facilitates a **timely** and **transparent** resolution of proposed modifications

Types of PMRs


1. Consistent with SIP

- Schedule change or minor scope/benefit modifications with no impact to future funding allocations




2. Inconsistent with SIP

- Any modifications to the Funding Request
- Significant modifications to Scope and/or Benefits

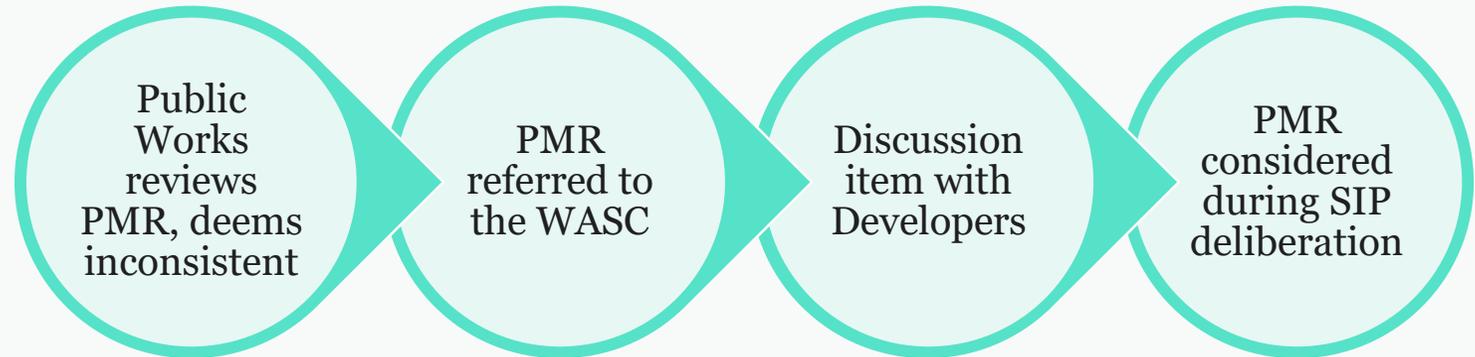

Overview of PMR SIP Deliberation

- Deem modified project as no longer meeting SCWP Goals, remove all projected SCWP funding or abandon modification
- Deem modified project as meeting SCWP Goals, and continue to support only the original funding request (no additional funding)
- Deem modified project as meeting SCWP Goals, and adjust funding in line with request, up to the amount requested in PMR



WASC Role in the PMR Process

Potential questions for the Recipient:

1. Would the additional funding request be the **only option** that would allow the project to be implemented?
2. Would **delaying funding allocations** impact the project's ability to be implemented?
3. Would funding only a **portion** of the additional funding request impact the project's ability to be implemented?
4. If a Recipient has multiple projects under consideration, which projects are the **highest priority** for the Recipient?
5. Has the Recipient considered **other funding sources**?

Round 7 Submitted PMRs

For PMRs received prior to or on October 31, 2025, the PMR will be considered for WASC's approval during the preparation of the FY26-27 SIP

ULAR (1 of 4)

Project Name	Program	Project Developer	Modification Details	Change Amount Requested (\$)	Determination
Westmont - Vermont Avenue Green Improvement	IP	LA County Public Works	Schedule Change - change in funded activity completion date	N/A	Consistent
Walnut Park Pocket Park Project	IP	County of Los Angeles	Schedule Change – change in funded activity completion date	N/A	Consistent
Arroyo Seco-San Rafael Treatment Wetlands	IP	City of Pasadena	Schedule Change - change in funded activity completion date	N/A	Consistent
Hollenbeck Park Lake Rehabilitation Project	IP	City of LA - LASAN	Schedule Change - change in funded activity completion date	N/A	Consistent
Sylmar Channel Project	IP	Cit of LA - LASAN	Schedule Change - change in funded activity completion date	N/A	Consistent
			Total Change Amount Requested	N/A	

ULAR (2 of 4)

Project Name	Program	Project Developer	Modification Details	Change Amount Requested (\$)	Determination
Eagle Rock Boulevard: A Multi-Modal Stormwater Capture	IP	City of LA - StreetsLA	Schedule Change - change in funded activity completion date	N/A	Consistent
Broadway-Manchester Multi-Modal Green Streets Project	IP	City of LA - StreetsLA	Schedule Change – change in funded activity completion date	N/A	Consistent
Lincoln Park Neighborhood Green Street Network	IP	City of LA - LASAN	Schedule Change – change in funded activity completion date	N/A	Consistent
Oro Vista Local Area Urban Flow Management Project	IP	City of LA - LASAN	Schedule Change – change in funded activity completion date	N/A	Consistent
Lankershim Boulevard Local Area Urban Flow Management Network	IP	City of LA - LASAN	Schedule Change – change in funded activity completion date	N/A	Consistent
			Total Change Amount Requested	N/A	

ULAR (3 of 4)

Project Name	Program	Project Developer	Modification Details	Change Amount Requested (\$)	Determination
Green Street Demonstration Project on Main Street	IP	City of Alhambra	Community Investment Benefits reduction (removal of recreational park area)	N/A	Inconsistent (WASC to deliberate)
Rory M. Shaw Wetlands Park Project	IP	LA County Flood Control District	Correction to Water Supply Benefits (Reduced)	N/A	Inconsistent (WASC to deliberate)
Watts Civic Center Serenity Greenway	IP	City of LA, CD 15	Increase funding request	+\$778,127 (+29.2%)	Inconsistent (WASC to deliberate)
			Total Change Amount Requested	+\$778,127 (+29.2%)	

ULAR (4 of 4)

Project Name	Program	Project Developer	Modification Details	Change Amount Requested (\$)	Determination
Jackson Elementary School Stormwater Improvement Project	IP	Amigos de los Rios and Pasadena Unified School District	Separate into two projects and CEQA standing on categorical exemption	N/A	PMR Not Applicable
Winery Canyon Channel and Descanso Gardens Stormwater Capture and Reuse Project	IP	Descanso Gardens Foundation	Schedule Change (NO change in funded activity completion date)	N/A	PMR Not Needed
LAUSD Living Schoolyards Program Pilot	SS	TreePeople	Schedule Change (NO change in funded activity completion date)	N/A	PMR Not Needed
preSIP: A Platform for Watershed Science and Project Collaboration	SS	San Gabriel Valley Council of Governments	Schedule Change (NO change in funded activity completion date)	N/A	PMR Not Needed
			Total Change Amount Requested	N/A	

Thank you

QUESTIONS?

Contact

www.SafeCleanWaterLA.org

SafeCleanWaterLA@pw.lacounty.gov

833-ASK-SCWP
